



وزارة شؤون مجلس الوزراء  
MINISTRY OF CABINET AFFAIRS

# Weekly Status Report

**Executive view for the Sector Head · Wednesday, 27 August 2026**

**Digital Transformation Department**

Confidential

Overview

# Portfolio summary

93

Total items

All projects, releases & demands

73

Projects & enhancements

Active deliveries & releases

20

Demands


Backlog & requests

37

Live

Currently in production

## Items by entity / sector

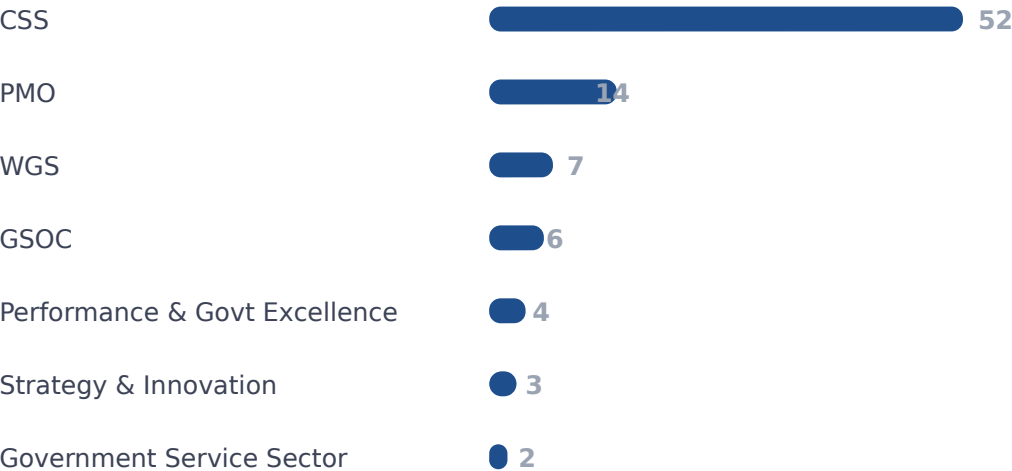

Section 01

Projects

| Project Name              | Entity / Sector | PM    | Current Status                                                                                                                                                                                                               | Next Steps                                                                                                                                                                      | Project Outcome                                        | Go Live                                                      |
|---------------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------|--------------------------------------------------------------|
| APEX-Contract Renewal     | CSS             | Banan | <ul style="list-style-type: none"><li>Closure</li><li>Finalizing the notification email is on hold due to Agentic AI P2P</li></ul>                                                                                           | Confirm next step with the project owner                                                                                                                                        | Automate the contract renewal process                  | TBD — We need to update the content of the email with the... |
| APEX-OutSource Hurring    | CSS             | Banan | <ul style="list-style-type: none"><li>Initiation</li><li>Revised plan has been shared with the business team</li></ul>                                                                                                       | Start the project                                                                                                                                                               | —                                                      | 12 Feb 2027                                                  |
| GSR Platform Enhancements | PMO             | Banan | <ul style="list-style-type: none"><li>On Track</li><li>Final video has been shared with TDRA for their assessment to approve moving the changes to production.</li><li>The requested feature is under development.</li></ul> | <ul style="list-style-type: none"><li>Share the final phase 3 UAT document for testing.</li><li>Finalize the feedback received from the business to start deployment.</li></ul> | Enhancements in the UX and work flow in the GSR system | 30 Sep 2026                                                  |
| Gov Survey Upgrade        | PMO             | Banan | <ul style="list-style-type: none"><li>On Track</li><li>Development is in progress, and the vendor is finalizing the build</li><li>The technical team initiates the TFS build</li></ul>                                       | Receive the final application build to begin staging deployment                                                                                                                 | To upgrade the Go survey tool                          | 19 Oct 2026                                                  |

| Project Name                   | Entity / Sector               | PM    | Current Status                                                                                                                                                                                                                            | Next Steps                                                                                                                                                             | Project Outcome                                                                                                        | Go Live                       |
|--------------------------------|-------------------------------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------|-------------------------------|
| MBRGEA                         | Performance & Govt Excellence | Banan | <ul style="list-style-type: none"><li>On Track</li><li>AI summarization and AI insight have been postponed for a week due to an urgent, high-priority feature from the business team ( invite link feature )</li></ul>                    | Resume development of AI summarization and AI insights after delivering the invite-link feature.                                                                       | Enhancement of the MBRGEA platform and implement the AI tool to facilitate the assessor assessment                     | 26 Oct 2026                   |
| MOCA Ride                      | CSS                           | Banan | <ul style="list-style-type: none"><li>Delayed by Business</li><li>Go-live meeting to align on next steps has been completed.</li><li>A few app-level changes were requested, shared with the vendor, and are under development.</li></ul> | Get the next step and final direction from the Chief: will the app be available to all MOCA employees or specific staff                                                | To have an application that dedicate for the ministry to have a ride services for the employee                         | TBD — Pending signed contract |
| Talent Managment System Design | CSS                           | Banan | <ul style="list-style-type: none"><li>On Track</li><li>The design phase is in progress</li><li>Kickoff meeting between Kalvad and tentwenty is complete; the Figma link has been shared with the development vendor</li></ul>             | <ul style="list-style-type: none"><li>Share the document that TenTwenty used to build the design.</li><li>Hold another meeting between Kalvad and TenTwenty.</li></ul> | To create a TMS UI/UX design for the new system with AI module to facilitate the assessment process and setting the... | 14 Oct 2026                   |

| Project Name                                                 | Entity / Sector | PM    | Current Status                                                                                                                                                                                                       | Next Steps                                                                                                                                                                                                                                                                                                                 | Project Outcome                                                                                                         | Go Live                                |
|--------------------------------------------------------------|-----------------|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------|----------------------------------------|
| UGAM Agentic AI Platform                                     | CSS             | Banan | <ul style="list-style-type: none"><li>On Track</li><li>IT kick-off completed</li><li>Security Kick-off completed</li><li>Milestone 1 - Registration and invitation requirements shared with Cohere</li></ul>         | <ul style="list-style-type: none"><li>Plan meetings for other milestones</li><li>Continue working on the IT infra with IT &amp; Cohere</li></ul>                                                                                                                                                                           | To develop a secure and flexible Agentic AI platform for the UAE Annual Government Meeting (UGAM). The platform will... | TBD — not yet baselined                |
| AI Chatbot                                                   | CSS             | Noura | <ul style="list-style-type: none"><li>On Track</li><li>Mohammed is working on the Manager tools.</li><li>There are 8 manager tools, and 3 of them have been completed:</li><li># List of Pending Approvals</li></ul> | <ul style="list-style-type: none"><li>Mohammed will start work on the remaining tools</li><li>Package preparation – 3 working days (update for manager features and current backend contract)</li><li>Design implementation phase will start once design is received (applying new design to existing interface)</li></ul> | Employees get a secure, embedded AI assistant that can accurately answer HR policy questions and directly handle...     | 7 Sep 2026                             |
| Automating the Group Email Creation Process - MOCA Smart App | CSS             | Noura | <ul style="list-style-type: none"><li>Initiation</li><li>We have shared the SP plan and the proposal with the business team.</li></ul>                                                                               | We are waiting for confirmation on whether the budget has been approved.                                                                                                                                                                                                                                                   | Faster, standardized, and trackable group email requests with less manual work for IT teams.                            | TBD — Currently finalizing the SP plan |

| Project Name                                         | Entity / Sector       | PM    | Current Status                                                                                                                                                                                                         | Next Steps                                                                                                                                                                                                                                                                                         | Project Outcome                                                                                                  | Go Live     |
|------------------------------------------------------|-----------------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|-------------|
| Automating the Group Email Creation Process - Oracle | CSS                   | Noura | <ul style="list-style-type: none"><li>On Track</li><li>The Oracle plan has been shared with the business team.</li></ul>                                                                                               | <ul style="list-style-type: none"><li>We have received the final proposal from the Kalvad team.</li><li>We are currently finalizing the SP plan and will share the complete project plan with the business team once it is finalized.</li></ul>                                                    | Faster, standardized, and trackable group email requests with less manual work for IT teams.                     | 19 Oct 2026 |
| Government Missions                                  | Strategy & Innovation | Noura | <ul style="list-style-type: none"><li>On Track</li><li>We had a meeting last week with FAHR, our technical team, and business to check whether FAHR provides another API or service that can retrieve the...</li></ul> | <ul style="list-style-type: none"><li>FAHR team shared the list of the entities that under the “Bayanati”</li><li>Business to share the list of entities is not within “Bayanati” System</li><li>Project team has confirmed that the integration be using Government Service Bus ( GSB )</li></ul> | Accelerate government innovation and execution by turning priority challenges into impactful solutions, while... | 1 Sep 2026  |

| Project Name                       | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                    | Next Steps                                                                                                                                                                                          | Project Outcome                                                                                                            | Go Live                 |
|------------------------------------|-----------------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|-------------------------|
| National Statistical Data Platform | FCSC            | Noura | <ul style="list-style-type: none"><li>In Progress</li><li>The project kicked off on 27/1/2026</li><li>It's currently in the discovery phase.</li><li>There are two discovery phases: a technology discovery phase focused on implementation and the tools to be used, and a business discovery phase...</li></ul> | <ul style="list-style-type: none"><li>Schedule a meeting with Presight to present the solution, scope and the roadmap. (Sasi)</li><li>Review RACI matrix and share the feedback. (Shamma)</li></ul> | —                                                                                                                          | TBD — not yet baselined |
| Northstar                          | PMO             | Noura | <ul style="list-style-type: none"><li>On Track</li><li>At this stage, the project is in the testing phase. The desktop application has already been developed, and the current focus is on implementing the...</li></ul>                                                                                          | Business to share the proposal, the project plan, and the list of users where the Northstar application needs to be deployed.                                                                       | Deliver an AI-powered desktop application that improves productivity and operational efficiency by leveraging Dragonfly... | TBD — not yet baselined |
| Stemexe                            | FCSC            | Noura | <ul style="list-style-type: none"><li>In Progress</li><li>Stemex is a system used to manage projects.</li><li>The project started two months ago.</li><li>The workflow has been deployed on FedNet.</li></ul>                                                                                                     | Confirm next step with the project owner                                                                                                                                                            | —                                                                                                                          | TBD — not yet baselined |

| Project Name | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                                                  | Next Steps                                                                                                                                                                                                                                                                                                                                                                                              | Project Outcome                                                                                                      | Go Live                                            |
|--------------|-----------------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------|----------------------------------------------------|
| Superset     | PMO             | Noura | <ul style="list-style-type: none"><li>In Progress</li><li>Superset is part of the PMS (Raqmnm) platform and serves as a subsite used for reporting and dashboard visualization.</li><li>Raqmn is live now, after security scan and everything, it was published as pms.egsep.ae, then project published with new url raqmnm.egsep.gae</li></ul> | Confirm next step with the project owner                                                                                                                                                                                                                                                                                                                                                                | —                                                                                                                    | TBD — not yet baselined                            |
| We the UAE   | PMO             | Noura | <ul style="list-style-type: none"><li>Delayed by Business</li><li>Business team has confirmed that Santhosh can proceed with updating the development link.</li><li>We are following up with Santhosh to share the update on the design.</li></ul>                                                                                              | <ul style="list-style-type: none"><li>The expected go-live is in August or September.</li><li>Once the content upload is completed, the team will proceed with integration, testing, and staging, which is expected to take approximately two weeks.</li><li>Santosh confirmed that once the Arabic content is finalized, the system can go live. The English content can be added afterward.</li></ul> | Deliver a modern, user-centric website with an enhanced visual design, improved navigation, and an optimized user... | TBD — awaiting business direction (target Aug/Sep) |



| Project Name                     | Entity / Sector | PM     | Current Status                                                                                                                      | Next Steps                                                                                                       | Project Outcome                                                   | Go Live     |
|----------------------------------|-----------------|--------|-------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------|-------------|
| WGS API Development 2027         | WGS             | Shamma | <ul style="list-style-type: none"><li>On Track</li><li>Setup Completed</li></ul>                                                    | Development                                                                                                      | API Gateway for all WGS platform Integration                      | 31 Dec 2026 |
| WGS Community Portal 2027        | WGS             | Shamma | <ul style="list-style-type: none"><li>Initiation</li><li>Not yet started</li></ul>                                                  | Continue on finalizing requirements                                                                              | Uplifting Community Portal for WGS 2027                           | 31 Dec 2026 |
| WGS Mobile App 2027              | WGS             | Shamma | <ul style="list-style-type: none"><li>Initiation</li><li>Wireframe completed</li></ul>                                              | <ul style="list-style-type: none"><li>Get final feedback and get it signed off</li><li>To start design</li></ul> | Uplifting mobile app for WGS 2027                                 | 31 Dec 2026 |
| WGS Program Portal 2027          | WGS             | Shamma | <ul style="list-style-type: none"><li>On Track</li><li>All requirements and session completed between business and vendor</li></ul> | <ul style="list-style-type: none"><li>Sign off requirements</li><li>Integration with salesforce</li></ul>        | Uplifting Program Portal for WGS 2027                             | 31 Dec 2026 |
| WGS Salesforce Enhancements 2027 | WGS             | Shamma | <ul style="list-style-type: none"><li>On Track</li><li>Finalizing the requirements</li></ul>                                        | Start development                                                                                                | Enhancing Salesforce Features for operations in different streams | 13 Jan 2027 |
| WGS Website 2027                 | WGS             | Shamma | <ul style="list-style-type: none"><li>Initiation</li><li>First Draft of wireframe completed</li></ul>                               | Implement the feedback                                                                                           | Uplifting Website for WGS 2027                                    | 31 Dec 2026 |

| Project Name                                 | Entity / Sector               | PM    | Current Status                                                                                                                                                                                                                                                                                                                                                   | Next Steps                                                                                                                                                | Project Outcome                                                                                                         | Go Live                                        |
|----------------------------------------------|-------------------------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------|------------------------------------------------|
| AI Board Observer - Cabinet                  | GSOC                          | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>We have completed all the 9 points which is sent by the minister, and the update has been sent to business after verification.</li><li>We have received additional 4 point from HE Khalid and the team is working on it.</li><li>New IPA has been sent to Business users to verify and confirm.</li></ul> | Closing the points on urgent bases and hand it over to business to verify and confirm.                                                                    | Supporting the cabinet and ministerial council members by providing insights on the meeting topics, best practice,...   | 31 Jan 2026<br>pending top management decision |
| AI Solution for KPI Insights Project in ADAA | Performance & Govt Excellence | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>Staging environment has been done, and the staging implemntation is done and system is working internally.</li><li>Weekly status has been taken in place.</li><li>UC4: Conversational AI (KPI Chatbot)</li></ul>                                                                                          | <ul style="list-style-type: none"><li>Finalizing the production environment.</li><li>Database initial study session</li><li>Finalize middleware</li></ul> | Analyzing existing data to summarize performance on ADAA system, provide actionable insights, forecast outcomes, and... | 30 Oct 2026                                    |

| Project Name                   | Entity / Sector           | PM    | Current Status                                                                                                                                                                                                                                                       | Next Steps                                                                                                                                                                                 | Project Outcome                                                                                                       | Go Live                                         |
|--------------------------------|---------------------------|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------|-------------------------------------------------|
| Agentic AI Committee Portal    | CSS                       | Zeyad | <ul style="list-style-type: none"><li>Initiation</li><li>Had an introduction meeting with Ayoub to get the last update.</li><li>Arranged a technical meeting with IT and business to discover the challenges and to define the roles and responsibilities.</li></ul> | Working with IT team to find a solution for the integration with ADAA and Khadamati.                                                                                                       | —                                                                                                                     | 30 Nov 2026                                     |
| Digital experience of the Code | Government Service Sector | Zeyad | <ul style="list-style-type: none"><li>In Progress</li><li>Had a status meeting with business this week.</li><li>Agree to host the solution on Fednet for this project phase.</li><li>Design phase started with Business.</li></ul>                                   | <ul style="list-style-type: none"><li>Plan a weekly status meeting with vendor and business.</li><li>Include the security team with the project to get their approval by 27-Aug.</li></ul> | Enables users to easily navigate, understand, and engage with the Code through advanced search, structured content... | TBD — Plan is still not submitted by the vendor |

| Project Name         | Entity / Sector           | PM    | Current Status                                                                                                                                                                                                                                                                                                                                                                 | Next Steps                                                                                                                                                                                                     | Project Outcome                                                                                                           | Go Live     |
|----------------------|---------------------------|-------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------|-------------|
| E-cabinet System 2.0 | GSOC                      | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>Working on data migration for current ecabinet activity with both vendors and prepare the infrastructure for documents migration.</li><li>BRD are approved from business.</li><li>Development is going on as the initial plan.</li></ul>                                                                                | <ul style="list-style-type: none"><li>Finalizing the documents in follow up system and moving it to pre-production environment.</li><li>Checking the outlook integration with Teknip team.</li></ul>           | Automating all GSoC processes which related to cabinet meeting which is : meeting, subjects, decision, correspondences... | 31 Oct 2026 |
| GovTech Radar        | Government Service Sector | Zeyad | <ul style="list-style-type: none"><li>In Progress</li><li>Raising a technical challenge to establish the integration channel between the platform which is on vendor tanent and Fednet. weekly status meeting...</li><li>Had technical meeting with the vendor to verify the solution of the data bus.</li><li>Weekly status meeting is done and status report sent.</li></ul> | <ul style="list-style-type: none"><li>Fetching and verification of the data sources from all systems by business users to confirm.</li><li>Follow up with vendor on the progress of the integration.</li></ul> | —                                                                                                                         | 31 Oct 2026 |

| Project Name      | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                                                                                | Next Steps                                                                                                                                                                                                                                            | Project Outcome                                                                             | Go Live     |
|-------------------|-----------------|-------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------|-------------|
| MBRGS Application | PMO             | Zeyad | <ul style="list-style-type: none"><li>In Progress</li><li>MBRGS has requested adjustments to the design brief to make it feel more premium, aspirational,</li><li>And human-centric — reflecting the calibre of the programme, its scholars, and its university</li><li>Partners. For the homepage, MBRGS suggests replacing the generic cityscape with H.H. Sheikh</li></ul> | <ul style="list-style-type: none"><li>A meeting is scheduled to discuss the final design of the website along with the suggestions that were made by MBRGS.</li><li>Align the project plan as per Maryam request to lunch the portal first.</li></ul> | Automatingthe full lifecycle of the Mohammed Bin Rashid Government Scholarships Program.    | 31 Dec 2026 |
| MBRGS Call Center | PMO             | Zeyad | <ul style="list-style-type: none"><li>In Progress</li><li>Toll number 800 has been requested and sent to Etisalat.</li><li>Escalate the delay of Etisalat response to our account manager.</li><li>Upload the signed request form in B2B portal.</li></ul>                                                                                                                    | <ul style="list-style-type: none"><li>Will Keep following to start the SIP configuration with the vendor.</li><li>Sending the two resources candidates.</li></ul>                                                                                     | Call center to answer all calls of the Mohammed Bin Rashid Government Scholarships Program. | 27 Nov 2026 |

| Project Name         | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                 | Next Steps                                                                                                                                                                                               | Project Outcome                                                                                                            | Go Live     |
|----------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------|-------------|
| Org Structure        | PMO             | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>UAT sessions continued this week where we collect the feedback and notes from business.</li><li>We target to close all pending UAT items by 2-Sep.</li><li>External entities UAT sessions which will planned to be on 20-Aug.</li></ul> | <ul style="list-style-type: none"><li>Continue UAT session with business user.</li><li>Closing the security findings.</li><li>Preparing the production environment to be ready for going-live.</li></ul> | Automate the process of approving the Org Structure for the federal entities and empower the users with the information... | 31 Aug 2026 |
| SecureAware Platform | CSS             | Zeyad | <ul style="list-style-type: none"><li>In Progress</li><li>Security scan on the code has been done and the report has sent to Asma to rectify the code.</li><li>Below is the security findings:</li><li>Fix the SQL Injection issue and restrict schema-file modification.</li></ul>            | Prepare the staging environment to host the application, after the security fix.                                                                                                                         | —                                                                                                                          | 31 Aug 2026 |

| Project Name                                                        | Entity / Sector             | PM    | Current Status                                                                                                                                                                                                                                                                                                                           | Next Steps                                                                                                                                                    | Project Outcome                                                                                                                | Go Live                                              |
|---------------------------------------------------------------------|-----------------------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------|
| UAE GLP Website Revamp                                              | Govt Leadership & Talent    | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>Website development is complete. staging environment has been done and solution has been deployed <a href="https://uaeglp-stg.moca.gov.ae">https://uaeglp-stg.moca.gov.ae</a></li><li>Sending to business users to test and confirm in order to moved it to production.</li></ul> | <b>CAB meeting is scheduled after we getting the confirmation from business users to go-live.</b>                                                             | <b>Redesign of the UAE government leaders programs by adding a new renovated website replacing the current.</b>                | <b>31 Aug 2026</b>                                   |
| UAE Regulatory Intelligence: Technical and Hosting services Project | Office of Secretary-General | Zeyad | <ul style="list-style-type: none"><li>On Track</li><li>Preparing for the phase 2 with vendor as the GPU hardware will be received by September.</li><li>Had technical meeting with our system team and vendor to finalize the approach of phase 2.</li></ul>                                                                             | <ul style="list-style-type: none"><li><b>Test and QA for the platform.</b></li><li><b>Close the security reported item from Cybersecurity team.</b></li></ul> | <b>Enabled AI-powered legislative drafting, reducing effort while identifying legal gaps and conflicts. Delivered an AI...</b> | <b>TBD — timeline unapproved; Phase 2 scope open</b> |

Section 02

MOCASmart

| Project Name                                   | Entity / Sector | PM    | Current Status                                                                                                                                                                          | Next Steps                                        | Project Outcome                                                                  | Go Live                                    |
|------------------------------------------------|-----------------|-------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------|----------------------------------------------------------------------------------|--------------------------------------------|
| Active releases                                |                 |       |                                                                                                                                                                                         |                                                   |                                                                                  |                                            |
| Release 5 - Business Mission                   | CSS             | Banan | <ul style="list-style-type: none"><li>On Track</li><li>Postpone business testing as the Business team requested until Monday, 8/31.</li></ul>                                           | Complete business testing and act on the feedback | Apply to a business mission through MOCA App                                     | 31 Jul 2026                                |
| On hold releases                               |                 |       |                                                                                                                                                                                         |                                                   |                                                                                  |                                            |
| MOCA Smart - Managerial & Executive Level View | CSS             | Banan | <ul style="list-style-type: none"><li>On Hold</li><li>Received direction to put this project on hold</li></ul>                                                                          | Confirm next step with the project owner          | Facilitate to track the employee attendance and leaves for the Executive manager | 18 Sep 2026                                |
| Future releases                                |                 |       |                                                                                                                                                                                         |                                                   |                                                                                  |                                            |
| MOCASmart Procurement Module                   | CSS             | —     | <ul style="list-style-type: none"><li>Not active</li><li>Received the proposal document from the vendor</li><li>Shared the proposal with the business team to obtain approval</li></ul> | Initiate the project                              | Not active as we need to know if we will do it through AI                        | TBD — not active - pending AI decision     |
| Peer Assignment System                         | CSS             | —     | <ul style="list-style-type: none"><li>Not active</li><li>Awaiting internal confirmation</li></ul>                                                                                       | Await HR confirmation                             | Not active as we are waiting for HR confirmation                                 | TBD — not active - pending HR confirmation |
| Working Remotely Enhancement                   | CSS             | —     | <ul style="list-style-type: none"><li>Not active</li><li>Meeting with the HR team scheduled for a brainstorming session</li></ul>                                                       | Hold the brainstorming session with the HR team   | Project Team need to reactive this request with HR                               | TBD — to be reactivated with HR            |



| Project Name       | Entity / Sector | PM    | Current Status | Next Steps | Project Outcome                                                                                                                                                                                                                                                                             | Go Live |
|--------------------|-----------------|-------|----------------|------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------|
| Delivered releases |                 |       |                |            |                                                                                                                                                                                                                                                                                             |         |
| Release 4.5        | CSS             | Banan | —              | —          | <ul style="list-style-type: none"><li>• Leave Visibility (FYI)</li><li>• Leave History &amp; Attendance Report Enhancement</li></ul>                                                                                                                                                        | Live    |
| Release 4.4        | CSS             | Banan | —              | —          | <ul style="list-style-type: none"><li>• Gift Disclosure Enhancement</li><li>• Payslip Design Enhancement - MOCASmart</li><li>• Hajj Leave Enhancement</li><li>• Personalized Eid Al Adha Greeting Link</li><li>• Survey Push Notification</li></ul>                                         | Live    |
| Release 4.3        | CSS             | Banan | —              | —          | <ul style="list-style-type: none"><li>• Vendor Catalog &amp; Tiers Enhancement</li><li>• Reject Requests (Petty Cash, Reimbursement, Credit Card)</li><li>• Employee Address Update</li><li>• Enhancing the Submission for Compassionate Leave</li><li>• Survey Push Notification</li></ul> | Live    |

| Project Name | Entity / Sector | PM    | Current Status | Next Steps | Project Outcome                                                                                                                                                                                                       | Go Live |
|--------------|-----------------|-------|----------------|------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------|
| Release 4.2  | CSS             | Banan | —              | —          | <ul style="list-style-type: none"><li>News &amp; Announcements</li><li>Absence Statistics (Check-In &amp; Check-Out Time)</li><li>WFH Check-In / Check-Out</li></ul>                                                  | Live    |
| Release 4.1  | CSS             | Ghaya | —              | —          | <ul style="list-style-type: none"><li>Duaa Popup Feature</li><li>TMS Guide on MOCASmart</li><li>Gift Disclosure Integration with Oracle</li></ul>                                                                     | Live    |
| Release 4    | CSS             | Ghaya | —              | —          | <ul style="list-style-type: none"><li>Pop-up for Pending Justification</li><li>Change Password Feature</li><li>Policies Section</li><li>Duaa Icon &amp; Push Notification</li><li>Relative Declaration Card</li></ul> | Live    |
| Release 3    | CSS             | Banan | —              | —          | Released and in production                                                                                                                                                                                            | Live    |

Section 03

Demands

| Demand / Request                                                                                              | Entity / Sector | PM    | Current Status                                                                                                                                                                                    | Next Steps                                                                                                                         | Status               |
|---------------------------------------------------------------------------------------------------------------|-----------------|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Decrees (HR Services)                                                                                         | CSS             | Banan | <ul style="list-style-type: none"><li>With Business</li><li>New demo conducted for template feature on GovSign</li><li>HR liked this feature and would like to proceed</li></ul>                  | Await chief approval                                                                                                               | With Business        |
| HR Requests (Job Description Icon & Oracle Integration, Employee Benefits, Contracts and Acknowledgment page) | CSS             | Banan | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>HR confirmation is required to finalize the SOW</li></ul>                                                                      | <ul style="list-style-type: none"><li>Obtain the vendor's cost and time estimate</li><li>Obtain cost approval to proceed</li></ul> | Under Scope Analysis |
| So Lite                                                                                                       | PMO             | Banan | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Met with the business and vendor and gathered the requirements</li><li>Initiated the process with the technical team</li></ul> | Confirm with the business whether any support is required at this stage                                                            | Under Scope Analysis |
| Talent Management System/ Development                                                                         | CSS             | Banan | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Kickoff meeting between Tenttwenty and Kalvad is complete.</li></ul>                                                           | Share the final SOW that matches the final design                                                                                  | Under Scope Analysis |
| Application Development for Government Relations & Protocol Department                                        | CSS             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We have shared the proposal and proposals comparison with business team</li></ul>                                              | Waiting for business direction                                                                                                     | Under Scope Analysis |

| Demand / Request                                                  | Entity / Sector | PM    | Current Status                                                                                                                                                                           | Next Steps                                                                                                                                                                                                                                                                                                                                                                              | Status               |
|-------------------------------------------------------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Assets requests                                                   | CSS             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We had a meeting with Motion Pexels and the business team to review the solution and gather their feedback.</li></ul> | <ul style="list-style-type: none"><li>Motion Pexels team will share the technical proposal, initial plan and cost that includes AI recommendations.</li><li>Saif and Shaikha will provide details of existing systems and API access information for Span, and other data sources to enable integrations.</li><li>Saif &amp; Shaikha will send a sample of the client's data.</li></ul> | Under Scope Analysis |
| Automating the department achievements report - Injaz-Enhancement | CSS             | Noura | <ul style="list-style-type: none"><li>Proposal Review</li><li>We received the proposal from kalvad team.</li></ul>                                                                       | <ul style="list-style-type: none"><li>We have shared the proposal with business</li><li>Multiple meetings were held with the business team and design team to discuss the Scope of Work. Additional changes have been requested, and once the...</li></ul>                                                                                                                              | Proposal Review      |

| Demand / Request                              | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                                           | Next Steps                                                                                                                                             | Status               |
|-----------------------------------------------|-----------------|-------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Avatar Ai Phase 2                             | PMO             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Explored the possibility of replicating the current avatar (same look and feel) to enable simultaneous deployment across multiple government...</li><li>The objective is to evolve the avatar from a single “minister” persona into an advisor supporting multiple ministers or government leadership teams.</li><li>Replicating the solution as a UAE national persona by adapting the avatar’s appearance and accent, while maintaining the same advisory function and...</li></ul> | Business team is awaiting vendor feedback on the previously shared questions regarding the proposed change of persona from "Minister" to "Advisor",... | Under Scope Analysis |
| Breathable Infrastructure Competition Website | PMO             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>The kickoff meeting is done with the business and the vendor to initiate the project.</li></ul>                                                                                                                                                                                                                                                                                                                                                                                       | Business team to share the content and branding guidelines                                                                                             | Under Scope Analysis |

| Demand / Request                                     | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                                        | Next Steps                                                                                                                                                                                                                                                                | Status               |
|------------------------------------------------------|-----------------|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Demand & Digital Transformation Services in MOCA App | CSS             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We had a meeting with the design team to discuss the changes, and we shared with them the feedback.</li></ul>                                                                                                                                                      | We are waiting for design team to share the updated design.                                                                                                                                                                                                               | Under Scope Analysis |
| Ems Phase 2                                          | CSS             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We had meeting with Evento team to discuss the redesign scope for the untested features that will be implemented.</li><li>The Agentic AI SOW was shared with the Evento team to review its feasibility. The team will check and confirm if it is doable.</li></ul> | <ul style="list-style-type: none"><li>It was agreed that the work will be divided into three separate scopes:</li><li># System Redesign &amp; Admin Page - No Additional Cost</li><li># Redesign of the existing system.</li></ul>                                        | Under Scope Analysis |
| GA Agentic AI Coach                                  | PMO             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We had two separate meeting with IT and cybersecurity team to kickoff the project.</li></ul>                                                                                                                                                                       | <ul style="list-style-type: none"><li>Capgemini team has shared the architecture design, list of questions, and details of the LLMs to be reviewed by shamma.</li><li>The project team will share the security questionnaire and data classification documents.</li></ul> | Under Scope Analysis |

| Demand / Request                                           | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                                                                                                                                  | Next Steps                                                                                                                                                                                                                                                                                          | Status               |
|------------------------------------------------------------|-----------------|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Photographer and Videographer Requests ( EMS and MOCA App) | CSS             | Noura | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>MOCA Smart will be used by employees to submit requests for photographers and videographers.</li><li>Admin users in EMS will be able to add/edit photographer and videographer schedules and show their leaves from Oracle.</li><li>In EMS, photographers will have the option to click “Start Job” when they begin and “End Job” upon completion.</li></ul> | <ul style="list-style-type: none"><li>The business team has decided to include Agentic AI in the project scope. We are currently updating the Scope of Work (SOW) and will share the...</li><li>Kalvad has shared the estimate, and we will have meeting tomorrow to discuss the AI part.</li></ul> | Under Scope Analysis |
| Store Management System                                    | CSS             | Noura | <ul style="list-style-type: none"><li>RFI</li><li>Business team will not proceed with in-house development and We have shared the SOW with several vendors, and we expect to receive their proposals by...</li><li>We are working on proposals comparison.</li></ul>                                                                                                                                                            | We will schedule a meeting with the business team to review and evaluate.                                                                                                                                                                                                                           | RFI                  |

| Demand / Request                            | Entity / Sector | PM    | Current Status                                                                                                                                                                       | Next Steps                                                                                                                                    | Status               |
|---------------------------------------------|-----------------|-------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------|----------------------|
| Automating the Cabinet Health-Check Process | GSOC            | Zeyad | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Scope and design has been highlighted to the vendor, and we expect the first release to be on July-2026</li></ul> | Having live demo with business once the release to deployed                                                                                   | Under Scope Analysis |
| Agentic AI - Finance MVP -Inception         | CSS             | Manju | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Meeting scheduled on Monday to align on the MVP requirements</li></ul>                                            | Confirm next step with the demand owner                                                                                                       | Under Scope Analysis |
| Agentic AI - Finance MVP -PWC               | CSS             | Manju | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Pwc briefed on the MVP requirements for finance</li></ul>                                                         | Finance to confirm which process from budgeting they will be using for MVP                                                                    | Under Scope Analysis |
| Agentic AI - P2P MVP -1001                  | CSS             | Manju | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>Oracle team has started developing the APIs.</li></ul>                                                            | Completed APIs are handed over to the vendor (1001) for further development                                                                   | Under Scope Analysis |
| Agentic AI - P2P MVP -Cohere                | CSS             | Manju | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>All alignments completed with cohere</li></ul>                                                                    | <ul style="list-style-type: none"><li>To start planning for the MVP development</li><li>Confirm IT &amp; Security perquisite if any</li></ul> | Under Scope Analysis |



| Demand / Request                 | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                  | Next Steps                                                                                          | Status               |
|----------------------------------|-----------------|-------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------|----------------------|
| Agentic AI - Payroll MVP -Aleria | CSS             | Manju | <ul style="list-style-type: none"><li>Under Scope Analysis</li><li>We had meetings with Aleria and they said only 2 process they will do on their environment with flat sheets</li><li>Chief confirmed to Shamma it should be on our prem and connected to the oracle</li></ul> | Aleria to get ack to us if they are willing to do the implementation on prem with Oracle connection | Under Scope Analysis |

Section 04

Live projects

| Project Name                             | Entity / Sector       | PM    | Go-Live     |
|------------------------------------------|-----------------------|-------|-------------|
| APEX- Off-Boarding                       | CSS                   | Banan | 8 May 2026  |
| APEX- Probation Extention                | CSS                   | Banan | 20 Mar 2026 |
| APEX- Relative Declaration               | CSS                   | Banan | 9 Mar 2026  |
| API Migration to OIC ( FORAS )           | CSS                   | Banan | 4 Dec 2025  |
| API Migration to OIC ( MocaVerse )       | CSS                   | Banan | 31 Dec 2025 |
| DOR                                      | CSS                   | Banan | 18 Mar 2026 |
| Enhancing MOCA Letters                   | CSS                   | Banan | 1 Apr 2026  |
| Events Calendar (MOCAverse)              | CSS                   | Banan | 28 Apr 2026 |
| Executive Dashboard Release 2-Enhancment | CSS                   | Banan | 13 May 2026 |
| Government Accelerator Website           | PMO                   | Banan | 30 Apr 2026 |
| Interactive Dashboard/Event website      | GSOC                  | Banan | 31 Aug 2026 |
| MOCA SSA                                 | CSS                   | Banan | 11 May 2026 |
| MOHAP Sick Leave Integration             | CSS                   | Banan | 24 Jul 2026 |
| NER                                      | CSS                   | Banan | Live        |
| Organization Structure (HR Services)     | CSS                   | Banan | 3 Aug 2026  |
| Talent Hub MBRCGI                        | Strategy & Innovation | Banan | Live        |
| Vendor Dashboard                         | CSS                   | Banan | 15 May 2026 |
| Vendor Management - NER Enhancement      | CSS                   | Banan | 29 Jul 2026 |
| WGS-Website                              | WGS                   | Banan | 19 Jan 2026 |

| Project Name                            | Entity / Sector               | PM     | Go-Live     |
|-----------------------------------------|-------------------------------|--------|-------------|
| Gift Disclosure Enhancment              | CSS                           | Ghaya  | 12 May 2026 |
| Avatar AI                               | PMO                           | Noura  | 31 Mar 2026 |
| Event Management System                 | CSS                           | Noura  | 9 Apr 2025  |
| Customer Pulse                          | Performance & Govt Excellence | Shamma | 31 Dec 2025 |
| AGEA System                             | Performance & Govt Excellence | Zeyad  | 12 Dec 2025 |
| Candidate Recruitment Committee Website | GSOC                          | Zeyad  | 30 Sep 2026 |
| GEEP                                    | GEEO                          | Zeyad  | 15 May 2026 |
| GSOC emp worksheet                      | GSOC                          | Zeyad  | 15 May 2026 |
| Innovation Ecosystem                    | Strategy & Innovation         | Zeyad  | 24 Nov 2025 |

Section 05

On hold / not active

| Project Name                                             | Entity / Sector | PM     | Current Status                                                                                                                                                                                                                                                                                                                                              | Next Steps                                                                                                                                                                                                         | Project Outcome                                                                                                        | Go Live                                             |
|----------------------------------------------------------|-----------------|--------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------|
| FAHR sick leave Integration                              | CSS             | Banan  | <ul style="list-style-type: none"><li>On Hold</li><li>On Hold due to Agentic AI P2P project</li></ul>                                                                                                                                                                                                                                                       | Resume development                                                                                                                                                                                                 | To have integration real time with sick leave with committee approvals                                                 | 23 Nov 2026                                         |
| Digital Library                                          | CSS             | Noura  | <ul style="list-style-type: none"><li>On Hold</li><li>We had a meeting with the AI Office and the vendor to review the proposed solution.</li><li>During the discussion, Saqr suggested adding an MCP layer on top of the solution. This would simplify future integrations and enhance the scalability...</li><li>As an example, if Fouzia asks:</li></ul> | <ul style="list-style-type: none"><li>The Media Info team will confirm if adding the MCP layer is feasible</li><li>Khawla will start filter the content</li><li>Kickoff meeting</li></ul>                          | —                                                                                                                      | TBD — not yet baselined                             |
| Media Monitoring & Public Feedback Intelligence Platform | PMO             | Zeyad  | <ul style="list-style-type: none"><li>On Hold</li><li>Vendor evaluation in under process by business users and procurement. reminder sent to business. there is some issue in the budgeting.</li></ul>                                                                                                                                                      | <ul style="list-style-type: none"><li>Finalize the vendor evaluation process with business users.</li><li>If there is no update from budgeting will move this project to on-hold until budget allocated.</li></ul> | Enhance the quality, responsiveness, and customer-centricity of government services across the UAE by observing and... | TBD — under technical evaluation; plan not provided |
| Project Dashboard in Executive Dashboard                 | CSS             | Shamma | <ul style="list-style-type: none"><li>On Hold</li><li>Waiting for the developer budget to be approved to onboard the developer</li></ul>                                                                                                                                                                                                                    | Once budget approved onboarding the developer to kick off the project                                                                                                                                              | —                                                                                                                      | TBD — not yet baselined                             |

Section 06

Not active / closed demands

| Demand / Request             | Entity / Sector | PM    | Current Status                                                                                                                                                                                                         | Next Steps                                                                                                                                     | Status                                                                                                  |
|------------------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------|
| Executive Dashboard Sprint 3 | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>Fouzia approved to do development once new developer onboarded</li></ul>                                                                                      | Once developer joined a plan will created for development                                                                                      | Not active as we are waiting if we will hire developer or with AI                                       |
| Onboarding (HR Services)     | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>Met with Ali to discuss next steps</li><li>We will await confirmation on whether this service will fall within the scope of the Agentic AI project.</li></ul> | <ul style="list-style-type: none"><li>Once a direction is provided, we will determine how to proceed accordingly.</li><li>Not active</li></ul> | Not active waiting for business direction                                                               |
| Payroll Bot Implementation   | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>On hold</li></ul>                                                                                                                                             | To select vendor                                                                                                                               | Not active moving to new platform                                                                       |
| Peer Assignment System       | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>Awaiting internal confirmation</li></ul>                                                                                                                      | Not Active                                                                                                                                     | Not active as we are waiting for HR confirmation                                                        |
| Promotion Project            | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>Created draft SOW and shared with Business for approval</li><li>Requested additional information needed to finalize the SOW</li></ul>                         | Finalize SOW and start the development                                                                                                         | Not active — automate the employee promotion/increment process by enhancing the existing Oracle Apex... |
| Remote Work Balance for GMO  | GMO             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>GMO study completed; shared with Ali</li></ul>                                                                                                                | Await direction                                                                                                                                | Not Active as we are waiting for HR direction                                                           |

| Demand / Request                    | Entity / Sector | PM    | Current Status                                                                                                                                                                           | Next Steps                                                                                                                                                                                                                                                                             | Status                                                                                                        |
|-------------------------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------|
| Security Form (Data Classification) | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>Received the initial design from the UX team</li><li>Send the presentation to Moza to schedule a meeting with Fouzia.</li></ul> | <ul style="list-style-type: none"><li>Present to Fouzia the initial design.</li><li>Project team will draft the initial SOW after Fouzia's approval on the design.</li><li>The implementation of the form will be based on the old criteria until the new policy is approved</li></ul> | Not Active as we are waiting for direction                                                                    |
| Working Remotely Enhancement        | CSS             | Banan | Not active                                                                                                                                                                               | Confirm next step with the demand owner                                                                                                                                                                                                                                                | Not active — project Team need to reactive this request with HR                                               |
| X Employee Project                  | CSS             | Banan | <ul style="list-style-type: none"><li>Not active</li><li>The project on hold due to Agentic AI P2P</li></ul>                                                                             | Confirm next step with the demand owner                                                                                                                                                                                                                                                | Not active — pull employee data from Oracle using predefined questions and answers, analyze it to generate... |
| Audio Translator in Teams           | CSS             | Noura | <ul style="list-style-type: none"><li>Not active</li><li>The proposals were received and shared with the business for feedback</li></ul>                                                 | Confirm next step with the demand owner                                                                                                                                                                                                                                                | Not active as per business direction                                                                          |
| Synthetic Memories UAE              | PMO             | Noura | <ul style="list-style-type: none"><li>Not active</li><li>The vendor is still finalizing the proposal</li></ul>                                                                           | We are waiting for an update from the business                                                                                                                                                                                                                                         | Not active as per business direction                                                                          |

| Demand / Request                     | Entity / Sector | PM     | Current Status                                                                                                                                                                                                                                                                | Next Steps                                                                                                                                       | Status                                                |
|--------------------------------------|-----------------|--------|-------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------------------------------------------------------------------------------|-------------------------------------------------------|
| Tech Trial AWS                       | PMO             | Noura  | <ul style="list-style-type: none"><li>Not active</li><li>The project is currently with IBM and in the design presentation phase for leadership</li><li>We recommended the business to go through the proposal with the IT and cybersecurity teams before presenting</li></ul> | Arrange two separate meetings with the IT and Cybersecurity teams to review the requirements                                                     | Not active as per business direction                  |
| Customer Pulse Integration with Jira | CSS             | Shamma | Not active                                                                                                                                                                                                                                                                    | Confirm next step with the demand owner                                                                                                          | Not active moving to new platform                     |
| Acting project                       | CSS             | Manju  | <ul style="list-style-type: none"><li>Not active</li><li>The project has been postponed at the Business's request</li></ul>                                                                                                                                                   | <ul style="list-style-type: none"><li>Once the project is active - get the SOW approval from Business</li><li>Commence the development</li></ul> | Not active — to handle acting positions and decisions |

| Demand / Request                                   | Entity / Sector | PM    | Current Status                                                                                                                                                                                                                                                                                                         | Next Steps                                                           | Status                                                                                                        |
|----------------------------------------------------|-----------------|-------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------|
| Digital Transformation Project Portfolio for chief | CSS             | Manju | <ul style="list-style-type: none"><li>Not active</li><li>We have now the link via claude we are exploring how we can host on our environment</li><li>Meeting with IT &amp; security to discuss requirements</li><li>Security and Application team have a few open queries that needs to be addressed by Hana</li></ul> | Finalize the project requirement and prepare the SOW document        | Not active — to have a dashboard for the chief where she can see 3 reports weekly: WGS Report CSS projects... |
| Job description Agent                              | CSS             | Manju | <ul style="list-style-type: none"><li>Not active</li><li>Evaluating the scope and gathering project requirements from the Business.</li><li>Oracle team validating the requirements and confirming the feasibility.</li></ul>                                                                                          | Finalize the development approach and SOW, and initiate development. | Not active — to create Job description for all the employees                                                  |
| WGS Evento/Registration                            | WGS             | Manju | <ul style="list-style-type: none"><li>Not active</li><li>Initial meeting with WGSxEvento held and MOM shared</li></ul>                                                                                                                                                                                                 | Finalize the SOW, project plan and start the development             | Not active — simplify and enhance the WGS registration process                                                |
