




WORLD
GOVERNMENTS
SUMMIT

Digital Transformation Strategy 2027

STATUS REPORT

Programme at a Glance

WGS Digital Transformation 2027 — Internal Status Update

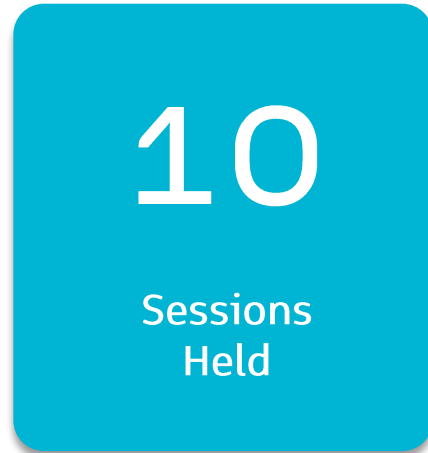

Overall Status- Report Update Covers

- | | |
|----------------------------|------------------------------------|
| 1 Meetings Held | 2 Program & Community Portal |
| 3 Salesforce & Integration | 4 Digital Platforms & DR Readiness |
| 5 Key Decisions & Risks | 6 Action Items & Next Steps |

Meetings Held — Week of 11 September 2026

10 sessions completed · 4 workstreams · Delivery & UAT readiness progressing

Programme Workstreams

O1 Program Portal ✓ Complete

Attendees

WGS · TenTwenty · MOCA

Key Outcomes

- Location management, screen exports and checklist modules reviewed with WGS and operational teams
- Checklist approval gates, notifications, presentation uploads and room/screen requirements aligned
- Hands-on end-to-end testing to follow once the UAT environment is ready
- 2027 scope exclusions reviewed, with selected items identified for leadership attention

O2 Salesforce & Integration ✓ Complete

Attendees

WGS · Salesforce · TenTwenty

Key Outcomes

- Program Portal ↔ Salesforce integration progressed across field mapping, picklists and synchronisation
- Daily sync plus manual synchronisation being developed using mock responses pending real MuleSoft APIs
- Salesforce Priority 1 — International Delegation — under implementation, targeted for 25 September
- Remaining Salesforce modules continue through solution design

O3 Website & Digital Experience ✓ Complete

Attendees

WGS · 1020

Key Outcomes

- Website branding reviewed against WGS guidelines
- Primary WGS blue to become more prominent across key digital elements
- WGS emblem / pattern to be incorporated selectively into the website design
- Website design to be revised and returned to WGS for brand review

Dominican Republic Readiness

O4 Dominican Republic Readiness ✓ Complete

Attendees

WGS · MOCA

Key Outcomes

- Priority Community Portal modules for DR reviewed with the business team
- DR live-streaming aligned at a high level — two venues and same-day YouTube delivery
- Existing WGS website will be used for DR rather than the new website
- Community Portal API planning started; delivery timeline remains a key DR dependency

Workstream Focus — Delivery & UAT Readiness

Moving from requirements into delivery and validation across all workstreams

Delivery Timeline



Current Status

- Program Portal functional validation advanced across location management, checklist, screen exports and presentation workflows
- Salesforce Priority 1 implementation underway; International Delegation targeted for completion by 25 September
- Program Portal ↔ Salesforce integration build progressing using mock responses while MuleSoft APIs are prepared
- Community Portal requirements for DR prioritised, with Salesforce API scope / timeline now requiring confirmation
- UAT / environment readiness remains an immediate technical focus, with outstanding configuration and access items being closed

Open Decisions

- Community Portal Timeline: confirm Salesforce / MuleSoft API scope and delivery timeline for DR-priority modules
- UAT Environment: close remaining environment / configuration issues to enable full end-to-end business testing
- 2027 Scope / Leadership Items: raise agreed scope limitations and delivery implications for leadership visibility
- Program Portal Operational Access: confirm final access / ownership approach for screen configuration and exports

Immediate Next Steps

- Close UAT environment and connectivity items and begin end-to-end business run-throughs
- Confirm Community Portal Phase 2 API scope and delivery timeline for DR
- Continue Salesforce Priority 1 implementation and remaining module solution designs
- Finalise Program Portal operational decisions and test key flows end-to-end in UAT

Salesforce & Integration — Current Status

11 September 2026 · Map → Build → Connect APIs → Test → Deploy



Priority 1 — International Delegation

IN IMPLEMENTATION. Implementation underway in Sprint 3, with completion targeted by 25 September 2026.



Remaining Enhancements

IN PROGRESS. Remaining Salesforce modules continue through solution design and WGS review.



Program Portal Integration

IN PROGRESS. TenTwenty is building the daily synchronisation and manual sync functionality using mock responses.



MuleSoft APIs — Real Integration

PENDING. Real API integration will follow once MuleSoft APIs and remaining mappings are ready.

Community Portal — Phase 2 / DR

TIMELINE TO CONFIRM. Community Portal API scope review has started; delivery timing needs to be confirmed against the DR requirement.

Access / Connectivity — Technical Access

IN PROGRESS. Programme Portal access has progressed; remaining VPN / DevOps connectivity items are being followed up.

Key Decisions & Risks

Items Requiring Management Attention Or Tracking

Open Decisions

Item	Detail	Status
Community Portal / DR Timeline	Confirm Phase 2 API scope and delivery timing to support the DR event.	Priority
2027 Scope Limitations	Selected out-of-scope / partial-delivery items require visibility — Coffee-Table Book, Post-Show Media Pack and Leadership Brief.	Raised
Program Portal Operational Access	Confirm whether the publicis receives restricted screen-configuration access or WGS retains update control.	Open Decision

Programme Risks

Level	Risk	Mitigation
HIGH	Community Portal DR Timeline	Community Portal API timing is not yet confirmed, creating a delivery risk against the November DR event. Mitigation: prioritise DR must-have modules and align Salesforce / MuleSoft API delivery with TenTwenty.
MED	Environment / UAT Readiness	Remaining SSL, service / configuration and access items may delay complete end-to-end UAT. Mitigation: close outstanding IT / TenTwenty items and verify the UAT environment before business run-throughs.

Action Items & Next Steps

Critical programme-level actions for the week ahead

Action Item	Owner	Target	Status
Confirm Community Portal Phase 2 API scope, priorities and delivery timeline for DR	Salesforce / MuleSoft / WGS / TenTwenty	Next Week	Priority
Close remaining UAT environment, connectivity and configuration items and begin end-to-end business run-throughs	WGS IT / TenTwenty	Immediate	In Progress
Continue Salesforce Priority 1 implementation and remaining module solution designs	Salesforce / WGS	25 Sep / Ongoing	In Progress
Finalise Program Portal operational decisions and test checklist, presentation and screen-export flows end-to-end	WGS / TenTwenty	On UAT	In Progress
