




WORLD
GOVERNMENTS
SUMMIT

Digital Transformation Strategy 2027

STATUS REPORT

Programme at a Glance

WGS Digital Transformation 2027 — Internal Status Update

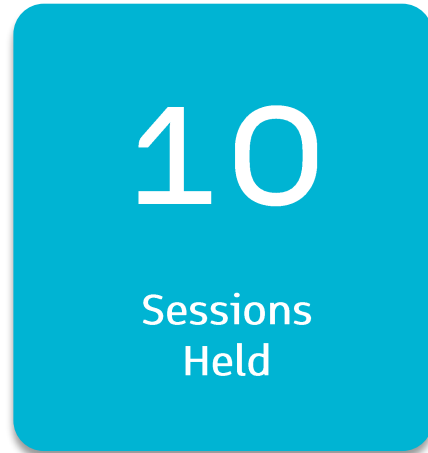

Overall Status- Report Update Covers

- | | |
|------------------------------|--|
| 1 Meetings Held | 2 DR & Platform Readiness |
| 3 Program & Community Portal | 4 Salesforce, Integration & Agentic AI |
| 5 Key Decisions & Risks | 6 Action Items & Next Steps |

Meetings Held — Week of 4 September 2026

10 sessions completed · 4 workstreams · DR readiness now driving priorities

Programme Workstreams

O1 DR & Platform Readiness ✓ Complete

Attendees

WGS · TenTwenty · Salesforce

Key Outcomes

- DR platform, registration, badging and operational readiness aligned
- New Program Portal planned as a real DR dry run, with existing system retained in parallel as backup
- Minimum Community Portal scope defined; DR data migration and operational preparation initiated
-

O2 Program & Community Portal ✓ Complete

Attendees

WGS · TenTwenty

Key Outcomes

- PCP / content validation progressed toward formal Program Portal sign-off
- Core Events → Programs → Sessions structure and terminology aligned
- Key program, participant, access and Community Portal journeys further defined
- Newspaper/export solution progressed; remaining requirements closing ahead of the November demo

O3 Salesforce & Integration ✓ Complete

Attendees

WGS · Salesforce · MuleSoft · 1020

Key Outcomes

- Salesforce Phase 1 integration mapping progressed toward build / testing
- API field-mapping review completed; updated API documentation and Postman collections being finalised
- International Delegation confirmed as first enhancement priority; detailed design underway, one feature in implementation
- VPN / connectivity is the current blocker preventing MuleSoft from testing 1020 APIs

Digital, Security & Agentic AI

O4 Digital, Security & Agentic AI ✓ Complete

Attendees

WGS · TenTwenty

Key Outcomes

- 4 Critical Agentic AI Capabilities Identified for detailed definition
- Security review progressed across Branch.io, NFC access-card login and AI models / data flows
- Website / mobile and livestreaming requirements progressed toward final validation

Workstream Focus — DR Readiness & Implementation

DR readiness now driving immediate delivery priorities across all workstreams

Delivery Timeline



Current Status

- DR is the immediate delivery priority, with the new Program Portal planned as the operational dry run
- Program Portal business validation is progressing toward formal sign-off
- Salesforce Phase 1 integration is moving toward build / testing, subject to connectivity
- Salesforce core enhancements have entered detailed design, with Priority 1 implementation already started
- 4 priority Agentic AI capabilities identified for detailed definition next week

Open Decisions

- MuleSoft Connectivity: WGS Security decision on VPN / IP-range to enable 1020 API testing
- Program Portal Sign-Off: close remaining PCP / business requirements for formal approval
- Salesforce Delivery Plan: confirm Wave 1 timing and enhancement delivery estimates
- Agentic AI Scope: agree workflows, integrations and delivery for the 4 priority capabilities
- Security: close remaining Branch.io, NFC login and AI model / data-flow confirmations

Immediate Next Steps

- Hold DR UAT milestone and progress toward pre-production
- Close Program Portal requirements and formal sign-off
- Unblock MuleSoft VPN / connectivity and start API testing
- Finalise Wave 1 integration and enhancement delivery plans
- Hold Agentic AI deep-dive on the 4 priority capabilities

Salesforce & Integration — Current Status

4 September 2026 · Two tracks: Integration / MuleSoft · Salesforce Core Enhancements



Phase 1 Integration

Moving toward testing. API field mappings reviewed; updated resource / API documentation and Postman collections being finalised.



MuleSoft Connectivity — BLOCKER

VPN access still pending WGS Security evaluation. Until connectivity is approved, MuleSoft cannot test against the 1020 environment.



Wave 1

Timeline required. Wave 1 readiness depends on connectivity and final API inputs; Salesforce / MuleSoft to confirm the Wave 1 timing and estimate.



Core Enhancements

Implementation started. International Delegation confirmed as Priority 1; ~8 features under detailed design with acceptance criteria, and one feature already approved and in implementation.

Enhancement Planning

Delivery plan required. Salesforce to complete detailed solution designs and story-level estimates and provide WGS with the overall enhancement delivery plan.

Next Step

Integration: Unblock Connectivity → Finalise APIs → Confirm Wave 1 → Test & Deliver. Enhancements: Design → Estimate → Review → Implement.

Key Decisions & Risks

Items Requiring Management Attention Or Tracking

Open Decisions

Item	Detail	Status
MuleSoft VPN / Connectivity	WGS Security to confirm the proposed VPN / IP-range approach so MuleSoft can connect to 1020 and begin API testing.	Priority / Pending
Program Portal Sign-Off	Close remaining PCP / business requirements and proceed with formal Program Portal approval.	In Progress
Salesforce Delivery Plan	Confirm Wave 1 integration timing and detailed Salesforce enhancement estimates / delivery plan.	Pending

Programme Risks

Level	Risk	Mitigation
HIGH	MuleSoft Connectivity	API testing cannot begin until MuleSoft receives connectivity to the 1020 environment. Mitigation: WGS Security to urgently assess and confirm the VPN / IP-range approach.
HIGH	DR Integration Timeline	DR readiness depends on timely Salesforce API integration, testing and environment readiness. Mitigation: prioritise DR-critical Wave 1 scope, unblock connectivity and track delivery dates.
MED	DR Data Migration	DR data requires cleansing and migration from the existing environment before production. Mitigation: prepare migration scripts early, run a dry run and complete WGS-led cleansing before production.

Action Items & Next Steps

Critical programme-level actions for the week ahead

Action Item	Owner	Target	Status
Resolve MuleSoft VPN / connectivity approval to enable API testing	WGS Security / Salesforce / MuleSoft	Immediate	Priority
Finalise API resource documentation, Postman collections and Wave 1 integration timeline	TenTwenty / Salesforce / MuleSoft	Next Week	In Progress
Close remaining Program Portal requirements and proceed to formal business sign-off	WGS / TenTwenty	Next Review	In Progress
Complete Salesforce Priority 1 enhancement designs/estimates and issue the enhancement delivery plan	Salesforce / WGS	Next Week	In Progress
Define the 4 priority Agentic AI capabilities: workflows, actions, integrations and delivery approach	WGS / TenTwenty	Next Week	Planned
