



وزارة شؤون مجلس الوزراء
MINISTRY OF CABINET AFFAIRS

Weekly Status Report

Executive view for the Sector Head · Wednesday, 29 July 2026

Digital Transformation Department

Confidential

Overview

Portfolio summary

86

Total items

All projects, releases & demands

70

Projects & enhancements

Active deliveries & releases

16

Demands


Backlog & requests

33

Live

Currently in production

Items by entity / sector

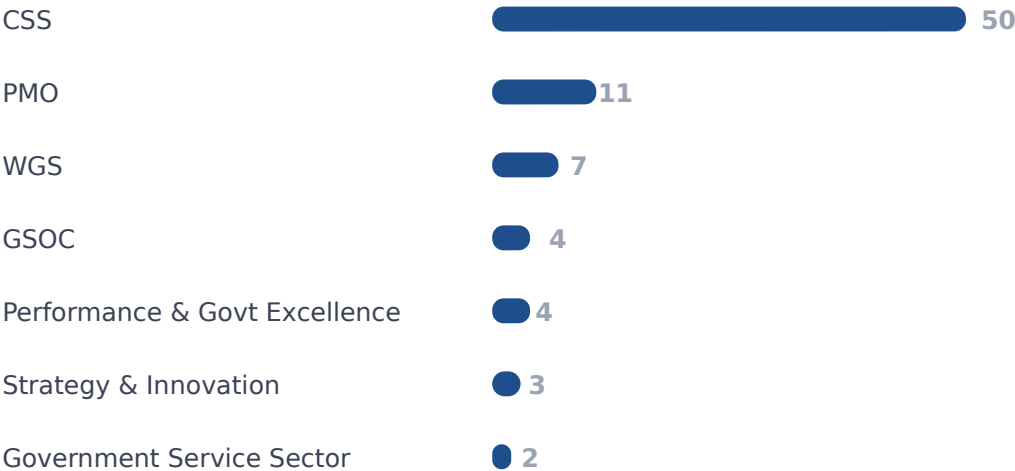

Section 01

Projects

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
APEX-Contract Renewal	CSS	Banan	- Closure - We received f/b for the email notification content to be updated from Ali - Content team updated the content based on Ali's f/b	- Oracle team to reflect the changes on the content of the email - Ali to review and give the final approval to close the project	Automate the contract renewal process	TBD — We need to update the content of the email with the...
APEX-OutSource Hurring	CSS	Banan	- Initiation - Revised plan has been shared with the business team	Start the project	—	12 Feb 2027
FAHR sick leave Integration	CSS	Banan	- On Track - Development in Progress	- Received the signed SOW - Continue the development	To have integration real time with sick leave with committee approvals	23 Nov 2026
GSR Platform Enhancements	PMO	Banan	- On Track - Meeting with TDRA has been completed and confirmed to UAE Pass as a sole log in mechanism - Solution has been sent to security check to perform the scan and has been passed successfully. - Request has been sent to CAB members to approve the going live.	Proceed with phase 2 deployment to production	Enhancements in the UX and work flow in the GSR system	30 Sep 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
MBRGEA	Performance & Govt Excellence	Banan	- On Track - The testing is in progress from the business side for the AI summarization tool and AI insight - New enhancement has been receive from the business side and its under development.	- Complete the ADAA integration enhancement - Complete the testing and get the UAT document sign off	Enhancement of the MBRGEA platform and implement the AI tool to facilitate the assessor assessment	26 Oct 2026
MOCA Ride	CSS	Banan	- Delayed by Business - The contract signing is still pending	- Contract to be signed - Vendor to do changes requested from business	To have an application that dedicate for the ministry to have a ride services for the employee	TBD — Pending signed contract
Organization Structure (HR Services)	CSS	Banan	- Closure - Waiting for HR to confirm that all the changes are reflected and reviewed.	Close the project	Build the Organization structure in oracle to reflect the changes without any manual work	3 Aug 2026
Talent Managment System Design	CSS	Banan	- On Track - Waiting for Patrick to share the prototype based on Chief's feedback so that it can be reviewed by her	Get the feedback after the demo.	To create a TMS UI/UX design for the new system with AI module to facilitate the assessment process and setting the...	21 Sep 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
AI Chatbot	CSS	Noura	- On Track - We went through the plan and the solution demo with business team. - The previous issue has been fixed.	- The password reset process will use a redirect link. The required steps and user guidance should be added. - The formatting, including text alignment, spacing, and layout, should be reviewed and standardized in both the Arabic and English versions.	Employees get a secure, embedded AI assistant that can accurately answer HR policy questions and directly handle...	7 Sep 2026
Automating the Group Email Creation Process - MOCA Smart App	CSS	Noura	- Initiation - We have received the final proposal from the Kalvad team.	We are currently finalizing the SP plan and will share the complete project plan with the business team once it is finalized.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	TBD — Currently finalizing the SP plan
Automating the Group Email Creation Process - Oracle	CSS	Noura	- On Track - The Oracle plan has been shared with the business team.	- We have received the final proposal from the Kalvad team. - We are currently finalizing the SP plan and will share the complete project plan with the business team once it is finalized.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	19 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Government Missions	Strategy & Innovation	Noura	- On Track - Reviewed the updated project timeline. The official launch remains 1 September, with some milestone dates adjusted. - Presented the high-level implementation plan covering the four project phases. - Agreed to complete the production go-live before the official launch to allow for testing and final validation.	- Amna to share the open files for the initiative logo and MBRCGI logo. - Update the platform header to include the initiative logo and government emblem/MBRCGI branding. - Provide additional graphic options for the landing page and challenge tracks.	Accelerate government innovation and execution by turning priority challenges into impactful solutions, while...	1 Sep 2026
National Statistical Data Platform	FCSC	Noura	- In Progress - The project kicked off on 27/1/2026 - It's currently in the discovery phase. - There are two discovery phases: a technology discovery phase focused on implementation and the tools to be used, and a business discovery phase...	- Schedule a meeting with Presight to present the solution, scope and the roadmap. (Sasi) - Review RACI matrix and share the feedback. (Shamma)	—	TBD — not yet baselined

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Stemexe	FCSC	Noura	- In Progress - Stemex is a system used to manage projects. - The project started two months ago. - The workflow has been deployed on FedNet.	Confirm next step with the project owner	—	TBD — not yet baselined
Superset	PMO	Noura	- In Progress - Superset is part of the PMS (Raqmn) platform and serves as a subsite used for reporting and dashboard visualization. - Raqmn is live now, after security scan and everything, it was published as pms.egsep.ae, then project published with new url raqmn.egsep.gae	Confirm next step with the project owner	—	TBD — not yet baselined

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
We the UAE	PMO	Noura	- Delayed by Business - We had a meeting last week with the business and vendor teams. - The business team requested changes to both the existing design and the new design. - Add an additional button on the Strategic page. Under the Scan QR Code section, add a button that allows users to contact the Director of Strategy.	- The expected go-live is in August or September. - Once the content upload is completed, the team will proceed with integration, testing, and staging, which is expected to take approximately two weeks. - Santosh confirmed that once the Arabic content is finalized, the system can go live. The English content can be added afterward.	—	TBD — awaiting business direction (target Aug/Sep)
WGS API Development 2027	WGS	Shamma	- Initiation - We are exploring shifting from eclrex to salesforce - Meetings with Salesforce completed to explain requirements	To finalize commercial engagement with Salesforce and kick-off with them	API Gateway for all WGS platform Integration	31 Dec 2026
WGS Community Portal 2027	WGS	Shamma	- Initiation - Not yet started	Continue on finalizing requirements	Uplifting Community Portal for WGS 2027	31 Dec 2026
WGS Mobile App 2027	WGS	Shamma	- Initiation - Not yet started	Confirm next step with the project owner	Uplifting mobile app for WGS 2027	31 Dec 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
WGS Program Portal 2027	WGS	Shamma	- Initiation - All requirements and session completed between business and vendor	To plan for a demo session to present to business progress on the development part	Uplifting Program Portal for WGS 2027	31 Dec 2026
WGS Salesforce Enhancements 2027	WGS	Shamma	- Initiation - We are exploring shifting from eclrex to salesforce - Meetings with Salesforce completed to explain requirements	To finalize commercial engagement with Salesforce and kick-off with them	Enhancing Salesforce Features for operations in different streams	13 Jan 2027
WGS Website 2027	WGS	Shamma	- Initiation - Not yet started	Confirm next step with the project owner	Uplifting Website for WGS 2027	31 Dec 2026
AI Board Observer - Cabinet	GSOC	Zeyad	- On Track - Data migration has been accomplished on staging (100 subjects) to verify the behavior of AI and to confirm it with business users before start on...	Fine tuning the data migration in staging along with all vendors to start the UAT with business users, before moving to production, as we are...	Supporting the cabinet and ministerial council members by providing insights on the meeting topics, best practice,...	31 Jan 2026 pending top management decision

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
AI Solution for KPI Insights Project in ADAA	Performance & Govt Excellence	Zeyad	- On Track - BRD has been approved by business users. - Development phase started. - Following up with IT team to finish the setup of staging enviroment.	Finalizing the staging and production environment. technical meeting will take place with application and system team by 03/Aug	Analyzing existing data to summarize performance on ADAA system, provide actionable insights, forecast outcomes, and...	30 Oct 2026
Candidate Recruitment Committee Website	GSOC	Zeyad	- In Progress - Providing access to Omar Altoukhy to TFS so that he can be able to push the code to staging. fixing the permission issue with Omar. new technical...	- Setting up the staging environment and pushing the source code. - Send it to security scan.	Provide a single source of truth for candidate profiles and their appointment status, streamline the pipeline. Give the...	30 Sep 2026
Digital experience of the Code	Government Service Sector	Zeyad	- In Progress - Had a status meeting with business this week. - Agree to host the solution on cloud for this project phase.	Plan a weekly status meeting with vendor and business, verify the AI LLM option with business.	Enables users to easily navigate, understand, and engage with the Code through advanced search, structured content...	TBD — Plan is still not submitted by the vendor

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
E-cabinet System 2.0	GSoC	Zeyad	- On Track - Working on data migration for current ecabinet activity with both vendors and prepare the infrastructure for documents migration. - BRD are approved from business. - Development is going on as the initial plan.	Finalizing the documents in follow up system and moving it to pre-production enviroment.	Automating all GSoC processes which related to cabinet meeting which is : meeting, subjects, decision, correspondences...	31 Oct 2026
GovTech Radar	Government Service Sector	Zeyad	- In Progress - Raising a technical challenge to establish the integration channel between the platform which is on vendor tanent and Fednet. weekly status meeting...	Contact Kalvad to setup the channel from the virtual data center which they manage to whitelist the vendor IPs.	—	31 Oct 2026
MBRGS Application	PMO	Zeyad	- In Progress - Design has been sent to Business. - Weekly meeting and report sent to business - Feedback from business users collected on the design.	- Rectify and update the design accordingly. - Technical meeting with TDRA for UAE Pass integration.	Automatingthe full lifecycle of the Mohammed Bin Rashid Government Scholarships Program.	31 Dec 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
MBRGS Call Center	PMO	Zeyad	- In Progress - Toll number 800 has been requested and sent to Etisalat. - Two resources under review by TEO.	Waiting IT team to upload the request in Etisalat B2B portal for number reservation to start the configuration. and align the business users about...	Call center to answer all calls of the Mohammed Bin Rashid Government Scholarships Program.	27 Nov 2026
Media Monitoring & Public Feedback Intelligence Platform	PMO	Zeyad	- Initiation - Vendor evaluation in under process by business users and procurement. reminder sent to business. there is some issue in the budgeting.	- Finalize the vendor evaluation process with business users. - If there is no update from budgeting will move this project to on-hold.	Enhance the quality, responsiveness, and customer-centricity of government services across the UAE by observing and...	TBD — under technical evaluation; plan not provided
Org Structure	PMO	Zeyad	- On Track - UAT sessions continued this week where we collect the feedback and notes from business. - First released of the staging after UAT has been deployed on Monday 27/07.	- Continue UAT session with business user. - Finalize the delivery date from the tracking sheet with business. - New Project plan to be prepared and send to business.	Automate the process of approving the Org Structure for the federal entities and empower the users with the information...	31 Aug 2026
UAE GLP Website Revamp	Govt Leadership & Talent	Zeyad	- On Track - Website development is complete. You can access the interactive version here: https://glp-uae.goldpro.cloud/en and its under review by business.	- We'll run one final feedback round, so please share any comments on the website. Right after that, we move into deployment preparation - Sending the site for security scan.	Redesign of the UAE government leaders programs by adding a new renovated website replacing the current.	31 Jul 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
UAE Regulatory Intelligence: Technical and Hosting services Project	Office of Secretary-General	Zeyad	- On Track - Preparing for the phase 2 with vendor as the GPU hardware will be received by September. - Had technical meeting with our system team and vendor to finalize the approach of phase 2.	- Test and QA for the platform. - Close the security reported item from Cybersecurity team.	Enabled AI-powered legislative drafting, reducing effort while identifying legal gaps and conflicts. Delivered an AI...	TBD — timeline unapproved; Phase 2 scope open

Section 02

MOCASmart

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Active releases						
Events Calendar (MOCASmart)	CSS	Banan	- On Track - Business tested the changes and shared additional feedback to Kalvad	Kalvad is working on the changes	Integrate the event calender in MOCAVerse to have in MOCA Smart	31 Jul 2026
Release 5 - Business Mission	CSS	Banan	- On Track - Internal testing is planned for today 29/7 - Internal testing will include feedback from the first session and the approval	Schedule the physical business testing next week	Apply to a business mission through MOCA App	31 Jul 2026
Release 4.6 - Managerial & Executive Level View	CSS	Banan	- On Track - Development in progress	Track development progress	Facilitate to track the employee attendance and leaves for the Executive manager	18 Sep 2026
Future releases						
MOCASmart Procurement Module	CSS	—	- Not active - Received the proposal document from the vendor - Shared the proposal with the business team to obtain approval	Initiate the project	Not active as we need to know if we will do it through AI	TBD — not active - pending AI decision

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Peer Assignment System	CSS	Banan	- Not active - Awaiting internal confirmation	Await HR confirmation	Not active as we are waiting for HR confirmation	TBD — not active - pending HR confirmation
HR Requests (Job Description Icon & Oracle Integration, Employee Benefits, Contracts, Acknowledgment Page)	CSS	—	- Under Scope Analysis - Draft SOW shared with the business; Job Description will be a separate scope	Await confirmation from the business	To add employees benefits and other HR enhancements	TBD — draft SOW awaiting confirmation
Working Remotely Enhancement	CSS	Banan	- Not active - Meeting with the HR team scheduled for a brainstorming session	Hold the brainstorming session with the HR team	Project Team need to reactive this request with HR	TBD — to be reactivated with HR
Delivered releases						
Release 4.5	CSS	Banan	—	—	- Leave Visibility (FYI) - Leave History & Attendance Report Enhancement	Live
Release 4.4	CSS	Banan	—	—	- Gift Disclosure Enhancement - Payslip Design Enhancement - MOCASmart - Hajj Leave Enhancement - Personalized Eid Al Adha Greeting Link - Survey Push Notification	Live

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Release 4.3	CSS	Banan	—	—	• Vendor Catalog & Tiers Enhancement • Reject Requests (Petty Cash, Reimbursement, Credit Card) • Employee Address Update • Enhancing the Submission for Compassionate Leave • Survey Push Notification	Live
Release 4.2	CSS	Banan	—	—	• News & Announcements • Absence Statistics (Check-In & Check-Out Time) • WFH Check-In / Check-Out	Live
Release 4.1	CSS	Ghaya	—	—	• Duaa Popup Feature • TMS Guide on MOCASmart • Gift Disclosure Integration with Oracle	Live
Release 4	CSS	Ghaya	—	—	• Pop-up for Pending Justification • Change Password Feature • Policies Section • Duaa Icon & Push Notification • Relative Declaration Card	Live

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Release 3	CSS	Banan	—	—	Released and in production	Live

Section 03

Demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Decrees (HR Services)	CSS	Banan	- With Business - New demo conducted for template feature on GovSign - HR liked this feature and would like to proceed	Await chief approval	With Business
Gov Survey upgrade	CSS	Banan	- Under Scope Analysis - Apply for a security clearance for the resource and waiting for the approval	To start project	Under Scope Analysis
HR Requests (Job Description Icon & Oracle Integration, Employee Benefits, Contracts and Acknowledgment page)	CSS	Banan	- Under Scope Analysis - We need to confirm the final Business Requirements and validate the full process flow	Meeting to be scheduled with HR to validate	Under Scope Analysis
Application Development for Government Relations & Protocol Department	CSS	Noura	- Under Scope Analysis - The SOW has been approved by the business team.	- We have invited the vendors to submit their proposals for the Government Relations & Protocol System - Mobile Application project. - The proposal submission deadline is 28 July.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Assets requests	CSS	Noura	- Under Scope Analysis - We had a meeting with Motion Pexels and the business team to review the solution and gather their feedback.	- Motion Pexels team will share the technical proposal, initial plan and cost that includes AI recommendations. - Saif and Shaikha will provide details of existing systems and API access information for Span, and other data sources to enable integrations. - Saif & Shaikha will send a sample of the client's data.	Under Scope Analysis
Automating the department achievements report - Injaz-Enhancement	CSS	Noura	- Proposal Review - We received the proposal from kalvad team.	- We have shared the proposal with business - Multiple meetings were held with the business team and design team to discuss the Scope of Work. Additional changes have been requested, and once the...	Proposal Review

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Avatar Ai Phase 2	PMO	Noura	- Under Scope Analysis - Explored the possibility of replicating the current avatar (same look and feel) to enable simultaneous deployment across multiple government... - The objective is to evolve the avatar from a single “minister” persona into an advisor supporting multiple ministers or government leadership teams. - Replicating the solution as a UAE national persona by adapting the avatar’s appearance and accent, while maintaining the same advisory function and...	Business team is awaiting vendor feedback on the previously shared questions regarding the proposed change of persona from "Minister" to "Advisor",...	Under Scope Analysis
Breathable Infrastructure Competition Website	PMO	Noura	- Under Scope Analysis - The business has approved to proceeding with awarding Planet Green as the vendor	We will schedule a kickoff meeting with the business and the vendor to initiate the project.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Demand & Digital Transformation Services in MOCA App	CSS	Noura	- Under Scope Analysis - The Scope of Work has been updated and approved. - We had a meeting with the design team to discuss the changes, and we shared with them the feedback.	We are waiting for design team to share the updated design.	Under Scope Analysis
Ems Phase 2	CSS	Noura	- Under Scope Analysis - We had a meeting with the Design Team and the Business Team. - The proposed design was approved.	- It was agreed that the work will be divided into three separate scopes: # System Redesign & Admin Page - No Additional Cost # Redesign of the existing system.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Photographer and Videographer Requests (EMS and MOCA App)	CSS	Noura	- Under Scope Analysis - MOCA Smart will be used by employees to submit requests for photographers and videographers. - Admin users in EMS will be able to add/edit photographer and videographer schedules and show their leaves from Oracle. - In EMS, photographers will have the option to click “Start Job” when they begin and “End Job” upon completion.	- Update - The business team has decided to include Agentic AI in the project scope. We are currently updating the Scope of Work (SOW) and will share the...	Under Scope Analysis
Store Management System	CSS	Noura	- RFI - Business team will not proceed with in-house development and We have shared the SOW with several vendors, and we expect to receive their proposals by...	Once we receive the proposals, we will schedule a meeting with the business team to review and evaluate.	RFI
UGAM Agentic AI Platform	CSS	Shamma	- Under Scope Analysis - Review the scope from project , IT & Security Aspects	Share updated scope with business	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Automating the Cabinet Health-Check Process	CSS	Zeyad	- Under Scope Analysis - Scope and design has been highlighted to the vendor, and we expect the first release to be on July-2026	Having live demo with business once the release to deployed	Under Scope Analysis
Acting project	CSS	Manju	- Under Scope Analysis - Draft SOW shared with HR to review and confirm	- Waiting for Marwa f/b on the SOW - If there is no f/b, a plan will be drafted and shared with Business approval	Under Scope Analysis
Digital Transformation Project Portfolio for chief	CSS	Manju	- In Progress - We have now the link via claude we are exploring how we can host on our environment - Meeting with IT & security to discusses requirements	The security team requested some changes and they will share list of requirements and inquires to be answered	In Progress

Section 04

Live projects

Project Name	Entity / Sector	PM	Go-Live
APEX- Off-Boarding	CSS	Banan	8 May 2026
APEX- Probation Extention	CSS	Banan	20 Mar 2026
APEX- Relative Declaration	CSS	Banan	9 Mar 2026
API Migration to OIC (FORAS)	CSS	Banan	4 Dec 2025
API Migration to OIC (MocaVerse)	CSS	Banan	31 Dec 2025
DOR	CSS	Banan	18 Mar 2026
Enhancing MOCA Letters	CSS	Banan	1 Apr 2026
Events Calendar (MOCAverse)	CSS	Banan	28 Apr 2026
Executive Dashboard Release 2-Enhancment	CSS	Banan	13 May 2026
Government Accelerator Website	PMO	Banan	30 Apr 2026
MOCA SSA	CSS	Banan	11 May 2026
MOHAP Sick Leave Integration	CSS	Banan	24 Jul 2026
NER	CSS	Banan	Live
Talent Hub MBRCGI	Strategy & Innovation	Banan	Live
Vendor Dashboard	CSS	Banan	15 May 2026
Vendor Management - NER Enhancement	CSS	Banan	29 Jul 2026
WGS-Website	WGS	Banan	19 Jan 2026
Gift Disclosure Enhancment	CSS	Ghaya	12 May 2026
Avatar AI	PMO	Noura	31 Mar 2026

Project Name	Entity / Sector	PM	Go-Live
Event Management System	CSS	Noura	9 Apr 2025
Customer Pulse	Performance & Govt Excellence	Shamma	31 Dec 2025
AGEA System	Performance & Govt Excellence	Zeyad	12 Dec 2025
GEEP	GEO	Zeyad	15 May 2026
GSOC emp worksheet	GSOC	Zeyad	15 May 2026
Innovation Ecosystem	Strategy & Innovation	Zeyad	24 Nov 2025

Section 05

On hold / not active

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Digital Library	CSS	Noura	- On Hold - We had a meeting with the AI Office and the vendor to review the proposed solution. - During the discussion, Saqr suggested adding an MCP layer on top of the solution. This would simplify future integrations and enhance the scalability... - As an example, if Fouzia asks:	- The Media Info team will confirm if adding the MCP layer is feasible - Khawla will start filter the content - Kickoff meeting	—	TBD — not yet baselined
Project Dashboard in Executive Dashboard	CSS	Shamma	- On Hold - Waiting for the developer budget to be approved to onboard the developer	Once budget approved onboarding the developer to kick off the project	—	TBD — not yet baselined

Section 06

Not active / closed demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Working Remotely Enhancement	CSS	Banan	Not active	Confirm next step with the demand owner	Not active — project Team need to reactive this request with HR
Onboarding (HR Services)	CSS	Banan	- Not active - Met with Ali to discuss next steps - We will await confirmation on whether this service will fall within the scope of the Agentic AI project.	- Once a direction is provided, we will determine how to proceed accordingly. - Not active	Not active waiting for business direction
Security Form (Data Classification)	CSS	Banan	- Not active - Received the initial design from the UX team - Send the presentation to Moza to schedule a meeting with Fouzia.	- Present to Fouzia the initial design. - Project team will draft the initial SOW after Fouzia's approval on the design. - The implementation of the form will be based on the old criteria until the new policy is approved	Not Active as we are waiting for direction
Executive Dashboard Sprint 3	CSS	Banan	- Not active - Fouzia approved to do development once new developer onboarded	Once developer joined a plan will created for development	Not active as we are waiting if we will hire developer or with AI
Remote Work Balance for GMO	GMO	Banan	- Not active - GMO study completed; shared with Ali	Await direction	Not Active as we are waiting for HR direction

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Payroll Bot Implementation	CSS	Banan	- Not active - On hold	To select vendor	Not active moving to new platform
Peer Assignment System	CSS	Banan	- Not active - Awaiting internal confirmation	Not Active	Not active as we are waiting for HR confirmation
Synthetic Memories UAE	PMO	Noura	- Not active - The vendor is still finalizing the proposal	We are waiting for an update from the business	Not active as per business direction
Audio Translator in Teams	CSS	Noura	- Not active - The proposals were received and shared with the business for feedback	Confirm next step with the demand owner	Not active as per business direction
Tech Trial AWS	PMO	Noura	- Not active - The project is currently with IBM and in the design presentation phase for leadership - We recommended the business to go through the proposal with the IT and cybersecurity teams before presenting	Arrange two separate meetings with the IT and Cybersecurity teams to review the requirements	Not active as per business direction
Customer Pulse Integration with Jira	CSS	Shamma	Not active	Confirm next step with the demand owner	Not active moving to new platform
