



وزارة شؤون مجلس الوزراء
MINISTRY OF CABINET AFFAIRS

Weekly Status Report — CSS

Executive view for the Sector Head · Wednesday, 9 September 2026

Digital Transformation Department

Confidential

Overview

Portfolio summary

52

Total items

All projects, releases & demands

37

Projects & enhancements

Active deliveries & releases

15

Demands


Backlog & requests

27

Live

Currently in production

Items by entity / sector

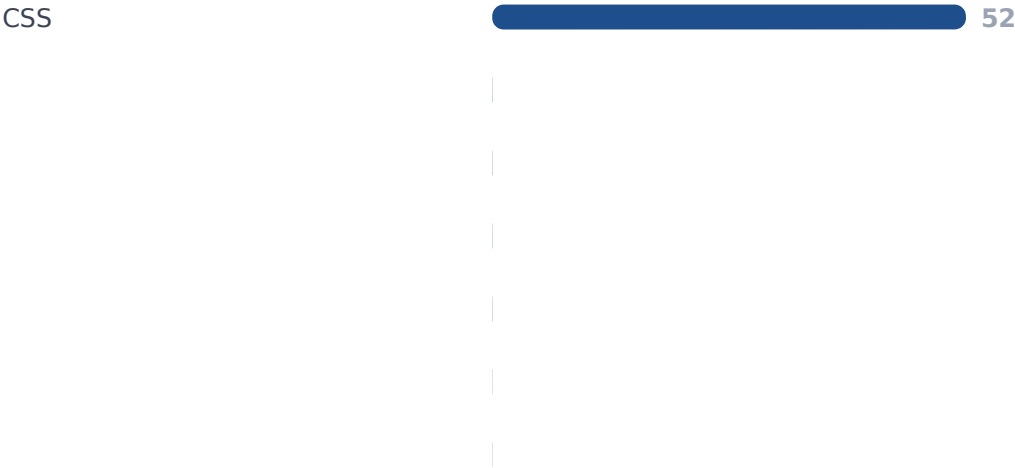

Section 01

Projects

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
APEX-Contract Renewal	CSS	Banan	- Closure - Finalizing the notification email is on hold due to Agentic AI P2P	Confirm next step with the project owner	Automate the contract renewal process	TBD — We need to update the content of the email with the...
APEX-OutSource Hurring	CSS	Banan	- Initiation - Revised plan has been shared with the business team	Start the project	—	12 Feb 2027
MOCA Ride	CSS	Banan	- Delayed by Business - The business requested a change to the approval process after a request is submitted and shared with the vendor. The business will confirm whether to...	Agree on the next step and an action plan for the approval process; it will require integration with Oracle.	To have an application that dedicate for the ministry to have a ride services for the employee	TBD — Pending signed contract
Talent Managment System Design	CSS	Banan	- On Track - Design is complete. We are waiting for documentation from tentwenty so the development vendor can start work.	Hold another meeting between Kalvad and TenTwenty.	To create a TMS UI/UX design for the new system with AI module to facilitate the assessment process and setting the...	14 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
UGAM Agentic AI Platform	CSS	Banan	- On Track - Access to our server has been granted to the vendor team - Received the updated architecture and the security questionnaire for the app from the vendor - Met with TDRA about registration portal integration with UAE PASS	- Finalize the first milestone after management approval - Get an update on milestone 2 - Schedule a meeting to proceed with milestone 3 — Scheduling & Allocation / Agenda	To develop a secure and flexible Agentic AI platform for the UAE Annual Government Meeting (UGAM). The platform will...	2 Nov 2026
AI Chatbot	CSS	Noura	- On Track - One tool was completed this week, bringing the total to 4 completed tools, with 4 remaining.	- Mohamed will start the design next week. - Noura will share the Manger tools use cases tomorrow.	Employees get a secure, embedded AI assistant that can accurately answer HR policy questions and directly handle...	7 Sep 2026
Automating the Group Email Creation Process - MOCA Smart App	CSS	Noura	- Initiation - We have shared the SP plan and the proposal with the business team.	We are waiting for confirmation on whether the budget has been approved.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	TBD — Currently finalizing the SP plan

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Automating the Group Email Creation Process - Oracle	CSS	Noura	- On Track - The Oracle plan has been shared with the business team.	- We have received the final proposal from the Kalvad team. - We are currently finalizing the SP plan and will share the complete project plan with the business team once it is finalized.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	19 Oct 2026
Agentic AI Committee Portal	CSS	Zeyad	- Initiation - Arranged a technical meeting with IT and business to discover the challenges and to define the roles and responsibilities. - Send the latest update code to IT by Ayoub.	Working with IT team to find a solution for the integration with ADAA and Khadamati.	—	30 Nov 2026

Section 02

MOCASmart

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Active releases						
Release 5 - Business Mission	CSS	Banan	- On Track - The changes have been completed, and business testing is scheduled for Thursday based on business availability.	Get business feedback and proceed accordingly	Apply to a business mission through MOCA App	21 Sep 2026
On hold releases						
MOCA Smart - Managerial & Executive Level View	CSS	Banan	- On Hold - Received direction to put this project on hold	Confirm next step with the project owner	Facilitate to track the employee attendance and leaves for the Executive manager	18 Sep 2026
Future releases						
MOCASmart Procurement Module	CSS	—	- Not active - Received the proposal document from the vendor - Shared the proposal with the business team to obtain approval	Initiate the project	Not active as we need to know if we will do it through AI	TBD — not active - pending AI decision
Peer Assignment System	CSS	—	- Not active - Awaiting internal confirmation	Await HR confirmation	Not active as we are waiting for HR confirmation	TBD — not active - pending HR confirmation
Working Remotely Enhancement	CSS	—	- Not active - Meeting with the HR team scheduled for a brainstorming session	Hold the brainstorming session with the HR team	Project Team need to reactive this request with HR	TBD — to be reactivated with HR

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Delivered releases						
Release 4.5	CSS	Banan	—	—	• Leave Visibility (FYI) • Leave History & Attendance Report Enhancement	Live
Release 4.4	CSS	Banan	—	—	• Gift Disclosure Enhancement • Payslip Design Enhancement - MOCASmart • Hajj Leave Enhancement • Personalized Eid Al Adha Greeting Link • Survey Push Notification	Live
Release 4.3	CSS	Banan	—	—	• Vendor Catalog & Tiers Enhancement • Reject Requests (Petty Cash, Reimbursement, Credit Card) • Employee Address Update • Enhancing the Submission for Compassionate Leave • Survey Push Notification	Live

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Release 4.2	CSS	Banan	—	—	- News & Announcements - Absence Statistics (Check-In & Check-Out Time) - WFH Check-In / Check-Out	Live
Release 4.1	CSS	Ghaya	—	—	- Duaa Popup Feature - TMS Guide on MOCASmart - Gift Disclosure Integration with Oracle	Live
Release 4	CSS	Ghaya	—	—	- Pop-up for Pending Justification - Change Password Feature - Policies Section - Duaa Icon & Push Notification - Relative Declaration Card	Live
Release 3	CSS	Banan	—	—	Released and in production	Live

Section 03

Demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Decrees (HR Services)	CSS	Banan	- With Business - New demo conducted for template feature on GovSign - HR liked this feature and would like to proceed	Await chief approval	With Business
HR Requests (Job Description Icon & Oracle Integration, Employee Benefits, Contracts and Acknowledgment page)	CSS	Banan	- Under Scope Analysis - HR confirmation is required to finalize the SOW	- Obtain the vendor's cost and time estimate - Obtain cost approval to proceed	Under Scope Analysis
Talent Management System/ Development	CSS	Banan	- Under Scope Analysis - Waiting for TenTwenty to share the document so we can finalize the scope.	Share the final SOW that matches the final design	Under Scope Analysis
Application Development for Government Relations & Protocol Department	CSS	Noura	- Under Scope Analysis - We have shared the proposal and proposals comparison with business team	Waiting for business direction	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Assets requests	CSS	Noura	- Under Scope Analysis - We had a meeting with Motion Pexels and the business team to review the solution and gather their feedback.	- Motion Pexels team will share the technical proposal, initial plan and cost that includes AI recommendations. - Saif and Shaikha will provide details of existing systems and API access information for Span, and other data sources to enable integrations. - Saif & Shaikha will send a sample of the client's data.	Under Scope Analysis
Automating the department achievements report - Injaz-Enhancement	CSS	Noura	- Proposal Review - We received the proposal from kalvad team.	- We have shared the proposal with business - Multiple meetings were held with the business team and design team to discuss the Scope of Work. Additional changes have been requested, and once the...	Proposal Review
Demand & Digital Transformation Services in MOCA App	CSS	Noura	- Under Scope Analysis - We had a meeting with Kalvad team to go through the design and SOW.	- We need to check with business if we will use Ivanti or Jira - Check if we will use the AI chatbot for the project requests	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Ems Phase 2	CSS	Noura	- Under Scope Analysis - We had meeting with Evento team to discuss the redesign scope for the untested features that will be implemented. - The Agentic AI SOW was shared with the Evento team to review its feasibility. The team will check and confirm if it is doable.	- It was agreed that the work will be divided into three separate scopes: # System Redesign & Admin Page – No Additional Cost # Redesign of the existing system.	Under Scope Analysis
Photographer and Videographer Requests (EMS and MOCA App)	CSS	Noura	- Under Scope Analysis - MOCA Smart will be used by employees to submit requests for photographers and videographers. - Admin users in EMS will be able to add/edit photographer and videographer schedules and show their leaves from Oracle. - In EMS, photographers will have the option to click “Start Job” when they begin and “End Job” upon completion.	- The business team has decided to include Agentic AI in the project scope. We are currently updating the Scope of Work (SOW) and will share the... - Kalvad has shared the estimate, and we will have meeting tomorrow to discuss the AI part.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Store Management System	CSS	Noura	- RFI - Proposals comparison are submitted to business	We are waiting for business directions.	RFI
Agentic AI - Finance MVP -PWC	CSS	Manju	- Under Scope Analysis - PWC briefed on the MVP requirements for finance - PWC requested for Budget control and I2P demo call on Thursday 10th Sep	- Finance to confirm which process from budgeting they will be using for MVP - Schedule the demo meeting upon confirmation	Under Scope Analysis
Agentic AI - P2P MVP -1001	CSS	Manju	- Under Scope Analysis - Shared the relevant Oracle API access and LLM, embedding model details. - Aligned with IT and Security - Oracle application access issue is being addressed with networks team	- Completed APIs are being progressively handed over to the vendor (1001) for further development. - Resolve the Oracle application access issue and other impediments arising during development	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Agentic AI - P2P MVP -Cohere	CSS	Manju	- Under Scope Analysis - Account creation completed; VPN and other relevant access permissions granted - Alignment meetings completed with the IT, Security, Oracle, and Business teams. - Shared the relevant Oracle API access and LLM details.	- Initiate MVP development planning. - Resolve the Oracle application access issue and other impediments arising during development	Under Scope Analysis
Agentic AI - P2P MVP -Inception	CSS	Manju	- Under Scope Analysis - Alignment meeting held with IT, Security and Oracle team - Account creation in progress	- Inception to come back with architecture and infrastructure plan for on-prem hosting - Inception to share security questionnaire for assessment	Under Scope Analysis
Agentic AI - Payroll MVP -Aleria	CSS	Manju	- Under Scope Analysis - To schedule a meeting with Aleria and we are waiting for their confirmation	Based on meeting outcome we will proceed	Under Scope Analysis

Section 04

Live projects

Project Name	Entity / Sector	PM	Go-Live
APEX- Off-Boarding	CSS	Banan	8 May 2026
APEX- Probation Extention	CSS	Banan	20 Mar 2026
APEX- Relative Declaration	CSS	Banan	9 Mar 2026
API Migration to OIC (FORAS)	CSS	Banan	4 Dec 2025
API Migration to OIC (MocaVerse)	CSS	Banan	31 Dec 2025
DOR	CSS	Banan	18 Mar 2026
Enhancing MOCA Letters	CSS	Banan	1 Apr 2026
Events Calendar (MOCAverse)	CSS	Banan	28 Apr 2026
Executive Dashboard Release 2-Enhancment	CSS	Banan	13 May 2026
MOCA SSA	CSS	Banan	11 May 2026
MOHAP Sick Leave Integration	CSS	Banan	24 Jul 2026
NER	CSS	Banan	Live
Organization Structure (HR Services)	CSS	Banan	3 Aug 2026
Vendor Dashboard	CSS	Banan	15 May 2026
Vendor Management - NER Enhancement	CSS	Banan	29 Jul 2026
Gift Disclosure Enhancment	CSS	Ghaya	12 May 2026
Event Management System	CSS	Noura	9 Apr 2025
SecureAware Platform	CSS	Zeyad	31 Aug 2026

Section 05

On hold / not active

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Digital Library	CSS	Noura	- On Hold - We had a meeting with the AI Office and the vendor to review the proposed solution. - During the discussion, Saqr suggested adding an MCP layer on top of the solution. This would simplify future integrations and enhance the scalability... - As an example, if Fouzia asks:	- The Media Info team will confirm if adding the MCP layer is feasible - Khawla will start filter the content - Kickoff meeting	—	TBD — not yet baselined
FAHR sick leave Integration	CSS	Banan	- On Hold - On Hold due to Agentic AI P2P project	Resume development	To have integration real time with sick leave with committee approvals	23 Nov 2026
Project Dashboard in Executive Dashboard	CSS	Shamma	- On Hold - Waiting for the developer budget to be approved to onboard the developer	Once budget approved onboarding the developer to kick off the project	—	TBD — not yet baselined

Section 06

Not active / closed demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Executive Dashboard Sprint 3	CSS	Banan	- Not active - Fouzia approved to do development once new developer onboarded	Once developer joined a plan will created for development	Not active as we are waiting if we will hire developer or with AI
Onboarding (HR Services)	CSS	Banan	- Not active - Met with Ali to discuss next steps - We will await confirmation on whether this service will fall within the scope of the Agentic AI project.	- Once a direction is provided, we will determine how to proceed accordingly. - Not active	Not active waiting for business direction
Payroll Bot Implementation	CSS	Banan	- Not active - On hold	To select vendor	Not active moving to new platform
Peer Assignment System	CSS	Banan	- Not active - Awaiting internal confirmation	Not Active	Not active as we are waiting for HR confirmation
Promotion Project	CSS	Banan	- Not active - Created draft SOW and shared with Business for approval - Requested additional information needed to finalize the SOW	Finalize SOW and start the development	Not active — automate the employee promotion/increment process by enhancing the existing Oracle Apex...

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Security Form (Data Classification)	CSS	Banan	- Not active - Received the initial design from the UX team - Send the presentation to Moza to schedule a meeting with Fouzia.	- Present to Fouzia the initial design. - Project team will draft the initial SOW after Fouzia's approval on the design. - The implementation of the form will be based on the old criteria until the new policy is approved	Not Active as we are waiting for direction
Working Remotely Enhancement	CSS	Banan	Not active	Confirm next step with the demand owner	Not active — project Team need to reactive this request with HR
X Employee Project	CSS	Banan	- Not active - The project on hold due to Agentic AI P2P	Confirm next step with the demand owner	Not active — pull employee data from Oracle using predefined questions and answers, analyze it to generate...
Audio Translator in Teams	CSS	Noura	- Not active - The proposals were received and shared with the business for feedback	Confirm next step with the demand owner	Not active as per business direction
Customer Pulse Integration with Jira	CSS	Shamma	Not active	Confirm next step with the demand owner	Not active moving to new platform
Acting project	CSS	Manju	- Not active - The project has been postponed at the Business's request	- Once the project is active - get the SOW approval from Business - Commence the development	Not active — to handle acting positions and decisions

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Digital Transformation Project Portfolio for chief	CSS	Manju	- Not active - We have now the link via claude we are exploring how we can host on our environment - Meeting with IT & security to discuss requirements - Security and Application team have a few open queries that needs to be addressed by Hana	Finalize the project requirement and prepare the SOW document	Not active — to have a dashboard for the chief where she can see 3 reports weekly: WGS Report CSS projects...
Job description Agent	CSS	Manju	- Not active - Evaluating the scope and gathering project requirements from the Business. - Oracle team validating the requirements and confirming the feasibility.	Finalize the development approach and SOW, and initiate development.	Not active — to create Job description for all the employes
