



وزارة شؤون مجلس الوزراء
MINISTRY OF CABINET AFFAIRS

Weekly Status Report

Executive view for the Sector Head · Wednesday, 9 September 2026

Digital Transformation Department

Confidential

Overview

Portfolio summary

97

Total items

All projects, releases & demands

73

Projects & enhancements

Active deliveries & releases

24

Demands


Backlog & requests

38

Live

Currently in production

Items by entity / sector

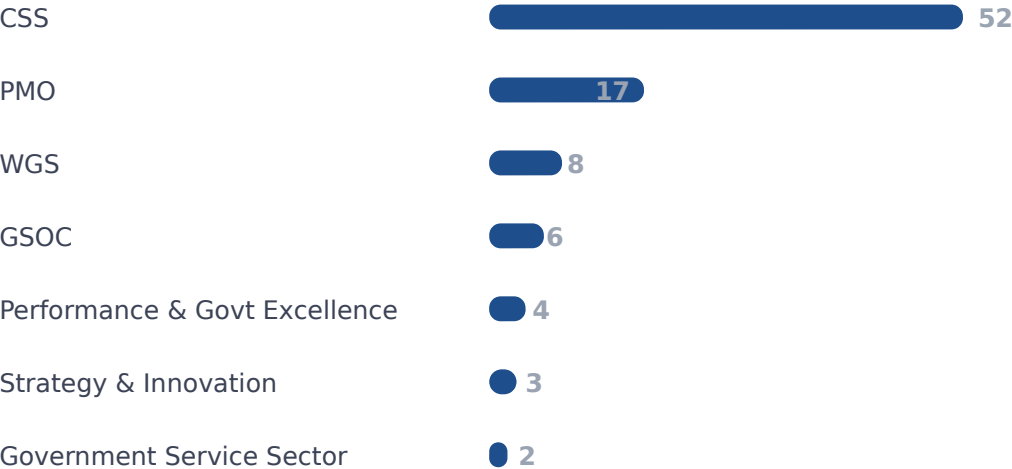

Section 01

Projects

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
APEX-Contract Renewal	CSS	Banan	- Closure - Finalizing the notification email is on hold due to Agentic AI P2P	Confirm next step with the project owner	Automate the contract renewal process	TBD — We need to update the content of the email with the...
APEX-OutSource Hurring	CSS	Banan	- Initiation - Revised plan has been shared with the business team	Start the project	—	12 Feb 2027
GSR Platform Enhancements	PMO	Banan	- On Track - The UAT document will be received at the end of this week, along with new features to be added in phase 3	Have a meeting with the vendor to discuss the new features.	Enhancements in the UX and work flow in the GSR system	30 Sep 2026
Gov Survey Upgrade	PMO	Banan	- On Track - The vendor sent the updated configuration for us to deploy. - We provisioned ten databases.	Complete the deployment and start vendor functionality testing.	To upgrade the Go survey tool	19 Oct 2026
MBRGEA	Performance & Govt Excellence	Banan	- On Track - AI insight, AI summarization, and KPI print dashboard UAT document has been shared with the business for testing.	Share the business feedback with the vendor and proceed with the deployment	Enhancement of the MBRGEA platform and implement the AI tool to facilitate the assessor assessment	26 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
MOCA Ride	CSS	Banan	- Delayed by Business - The business requested a change to the approval process after a request is submitted and shared with the vendor. The business will confirm whether to...	Agree on the next step and an action plan for the approval process; it will require integration with Oracle.	To have an application that dedicate for the ministry to have a ride services for the employee	TBD — Pending signed contract
Talent Managment System Design	CSS	Banan	- On Track - Design is complete. We are waiting for documentation from tentwenty so the development vendor can start work.	Hold another meeting between Kalvad and TenTwenty.	To create a TMS UI/UX design for the new system with AI module to facilitate the assessment process and setting the...	14 Oct 2026
UGAM Agentic AI Platform	CSS	Banan	- On Track - Access to our server has been granted to the vendor team - Received the updated architecture and the security questionnaire for the app from the vendor - Met with TDRA about registration portal integration with UAE PASS	- Finalize the first milestone after management approval - Get an update on milestone 2 - Schedule a meeting to proceed with milestone 3 — Scheduling & Allocation / Agenda	To develop a secure and flexible Agentic AI platform for the UAE Annual Government Meeting (UGAM). The platform will...	2 Nov 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
AI Chatbot	CSS	Noura	- On Track - One tool was completed this week, bringing the total to 4 completed tools, with 4 remaining.	- Mohamed will start the design next week. - Noura will share the Manger tools use cases tomorrow.	Employees get a secure, embedded AI assistant that can accurately answer HR policy questions and directly handle...	7 Sep 2026
Automating the Group Email Creation Process - MOCA Smart App	CSS	Noura	- Initiation - We have shared the SP plan and the proposal with the business team.	We are waiting for confirmation on whether the budget has been approved.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	TBD — Currently finalizing the SP plan
Automating the Group Email Creation Process - Oracle	CSS	Noura	- On Track - The Oracle plan has been shared with the business team.	- We have received the final proposal from the Kalvad team. - We are currently finalizing the SP plan and will share the complete project plan with the business team once it is finalized.	Faster, standardized, and trackable group email requests with less manual work for IT teams.	19 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Government Missions	Strategy & Innovation	Noura	- On Track - The application will be deployed on the existing Kubernetes environments. - The vendor team will require PMO IDs and access to push the code. - The vendor should focus on completing the application and providing the required code/deployment details; the internal team will handle the...	- Vendor to continue development and share the final code as early as possible. - Internal IT team to support the deployment on behalf of the vendor while their access is being processed. - Once the code is ready, IT will deploy it to staging and initiate the Cybersecurity scanning process.	Accelerate government innovation and execution by turning priority challenges into impactful solutions, while...	1 Sep 2026
National Statistical Data Platform	FCSC	Noura	- In Progress - The project kicked off on 27/1/2026 - It's currently in the discovery phase. - There are two discovery phases: a technology discovery phase focused on implementation and the tools to be used, and a business discovery phase...	- Schedule a meeting with Presight to present the solution, scope and the roadmap. (Sasi) - Review RACI matrix and share the feedback. (Shamma)	—	TBD — not yet baselined

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Northstar	PMO	Noura	- On Track - At this stage, the project is in the testing phase. The desktop application has already been developed, and the current focus is on implementing the...	Business to share the proposal, the project plan, and the list of users where the Northstar application needs to be deployed.	Deliver an AI-powered desktop application that improves productivity and operational efficiency by leveraging Dragonfly...	TBD — not yet baselined
Stemexe	FCSC	Noura	- In Progress - Stemex is a system used to manage projects. - The project started two months ago. - The workflow has been deployed on FedNet.	Confirm next step with the project owner	—	TBD — not yet baselined
Superset	PMO	Noura	- In Progress - Superset is part of the PMS (Raqlmn) platform and serves as a subsite used for reporting and dashboard visualization. - Raqlmn is live now, after security scan and everything, it was published as pms.egsep.ae, then project published with new url raqlmn.egsep.gae	Confirm next step with the project owner	—	TBD — not yet baselined

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
We the UAE	PMO	Noura	- Delayed by Business - Business team has confirmed that Santhosh can proceed with updating the development link. - We are following up with Santhosh to share the update on the design.	- The expected go-live is in August or September. - Once the content upload is completed, the team will proceed with integration, testing, and staging, which is expected to take approximately two weeks. - Santosh confirmed that once the Arabic content is finalized, the system can go live. The English content can be added afterward.	Deliver a modern, user-centric website with an enhanced visual design, improved navigation, and an optimized user...	TBD — awaiting business direction (target Aug/Sep)
WGS API Development 2027	WGS	Shamma	- On Track - Setup Completed	Development	API Gateway for all WGS platform Integration	31 Dec 2026
WGS Community Portal 2027	WGS	Shamma	- Initiation - Not yet started	Continue on finalizing requirements	Uplifting Community Portal for WGS 2027	31 Dec 2026
WGS Mobile App 2027	WGS	Shamma	- Initiation - Wireframe completed	- Get final feedback and get it signed off - To start design	Uplifting mobile app for WGS 2027	31 Dec 2026
WGS Program Portal 2027	WGS	Shamma	- On Track - All requirements and session completed between business and vendor	- Sign off requirements - Integration with salesforce	Uplifting Program Portal for WGS 2027	31 Dec 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
WGS Salesforce Enhancements 2027	WGS	Shamma	- On Track - Finalizing the requirements	Start development	Enhancing Salesforce Features for operations in different streams	13 Jan 2027
WGS Website 2027	WGS	Shamma	- Initiation - First Draft of wireframe completed	Implement the feedback	Uplifting Website for WGS 2027	31 Dec 2026
AI Board Observer - Cabinet	GSOC	Zeyad	- On Track - System has been launched successfully during Cabinet meeting.	# Restore the previous setup so that any agenda item added, deleted, or updated in the Smart Majlis is automatically reflected in the AI system, ... # Once the meeting brief has been reviewed, updated, and approved by H.E. Khalid AlHarmoodi or myself, the AI system should not make any further...	Supporting the cabinet and ministerial council members by providing insights on the meeting topics, best practice,...	31 Jan 2026 pending top management decision
AI Solution for KPI Insights Project in ADAA	Performance & Govt Excellence	Zeyad	- On Track - Staging environment has been done, and the staging implemntation is done and system is working internally. - Weekly status has been taken in place. - UC4: Conversational AI (KPI Chatbot)	- Finalizing the production environment. - Database initial study session - Finalize middleware	Analyzing existing data to summarize performance on ADAA system, provide actionable insights, forecast outcomes, and...	30 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Agentic AI Committee Portal	CSS	Zeyad	- Initiation - Arranged a technical meeting with IT and business to discover the challenges and to define the roles and responsibilities. - Send the latest update code to IT by Ayoub.	Working with IT team to find a solution for the integration with ADAA and Khadamati.	—	30 Nov 2026
Digital experience of the Code	Government Service Sector	Zeyad	- In Progress - Send the application to cybersecurity team to verify and check to provide their feedback. - Send the technical documentations to system & application team to start the hosting. - Requesting a technical meeting with vendor and IT team to agree on the hosting approach.	- Technical meeting with vendor and IT team to agree on the hosting approach. - Providing the new system archticture to be send to cyber team for their apporval.	Enables users to easily navigate, understand, and engage with the Code through advanced search, structured content...	TBD — Plan is still not submitted by the vendor

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
E-cabinet System 2.0	GSoC	Zeyad	- On Track - Working on data migration for current ecabinet activity with both vendors and prepare the infrastructure for documents migration. - Prepare the AI integration with the vendor to present it to HE Khalid.	- Present the AI integration approach with the suggested use cases to Khalid. - Verify the files migration with the vendor in help with the Sharepoint specialist.	Automating all GSoC processes which related to cabinet meeting which is : meeting, subjects, decision, correspondences...	31 Oct 2026
GovTech Radar	Government Service Sector	Zeyad	- In Progress - Agree on the hosting approach with business to move the application from AWS to Fednet to meet the integration points: - Khadamati, Tawasul 171, NCRM, RUM, Mystery shopper, Service Observatory, Customer pulse - Align with our IT team about the Fednet hosting option by providing them all the required documentations.	- Technical meeting with system and application team to agree about the app migration plan. - Filling the FedAI onboarding form to use Fednet AI service.	—	31 Oct 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
MBRGS Application	PMO	Zeyad	- In Progress - Held a review meeting with MBRGS to discuss the final design for the website; MBRGS requested minor adjustments related to the overall flow of the... - MBRGS requested additional changes to the website design; our design team has worked on and incorporated these changes. - MBRGS reviewed the website design and the Portal design and, following their feedback, confirmed that IT Max Global can proceed with the BRD...	- Proceed with completing the BRD - Prepare and share the UAT access links with MBRGS for their review ahead of launch. - Adjust the Project Plan once the BRD is finalized and share the updated details with MBRGS.	Automatingthe full lifecycle of the Mohammed Bin Rashid Government Scholarships Program.	31 Dec 2026
MBRGS Call Center	PMO	Zeyad	- In Progress - Toll number 800 has been requested and sent to Etisalat. - Escalate the delay of Etisalat response to our account manager. - Upload the signed request form in B2B portal.	- Will Keep following to start the SIP configuration with the vendor. - Sending the two resources candidates.	Call center to answer all calls of the Mohammed Bin Rashid Government Scholarships Program.	27 Nov 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Org Structure	PMO	Zeyad	- On Track - Completing work on changes requested in UAT and all the must have points has been done. - Requesting the advice for business for going-live date. - Production Environment Setup (For UAT Readiness)	Waiting business users approval on going-live.	Automate the process of approving the Org Structure for the federal entities and empower the users with the information...	31 Aug 2026
UAE GLP Website Revamp	Govt Leadership & Talent	Zeyad	- On Track - Website development is complete. staging environment has been done and solution has been deployed https://uaeglp-stg.moca.gov.ae - Sending to business users to test and confirm in order to moved it to production.	- CAB meeting is scheduled after we getting the confirmation from business users to go-live. - Design aproval required for the new Logo	Redesign of the UAE government leaders programs by adding a new renovated website replacing the current.	30 Sep 2026

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
UAE Regulatory Intelligence: Technical and Hosting services Project	Office of Secretary-General	Zeyad	- On Track - Preparing for the phase 2 with vendor as the GPU hardware will be received by September. - Had technical meeting with our system team and vendor to finalize the approach of phase 2.	- Test and QA for the platform. - Close the security reported item from Cybersecurity team.	Enabled AI-powered legislative drafting, reducing effort while identifying legal gaps and conflicts. Delivered an AI...	TBD — timeline unapproved; Phase 2 scope open

Section 02

MOCASmart

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Active releases						
Release 5 - Business Mission	CSS	Banan	- On Track - The changes have been completed, and business testing is scheduled for Thursday based on business availability.	Get business feedback and proceed accordingly	Apply to a business mission through MOCA App	21 Sep 2026
On hold releases						
MOCA Smart - Managerial & Executive Level View	CSS	Banan	- On Hold - Received direction to put this project on hold	Confirm next step with the project owner	Facilitate to track the employee attendance and leaves for the Executive manager	18 Sep 2026
Future releases						
MOCASmart Procurement Module	CSS	—	- Not active - Received the proposal document from the vendor - Shared the proposal with the business team to obtain approval	Initiate the project	Not active as we need to know if we will do it through AI	TBD — not active - pending AI decision
Peer Assignment System	CSS	—	- Not active - Awaiting internal confirmation	Await HR confirmation	Not active as we are waiting for HR confirmation	TBD — not active - pending HR confirmation
Working Remotely Enhancement	CSS	—	- Not active - Meeting with the HR team scheduled for a brainstorming session	Hold the brainstorming session with the HR team	Project Team need to reactive this request with HR	TBD — to be reactivated with HR

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Delivered releases						
Release 4.5	CSS	Banan	—	—	• Leave Visibility (FYI) • Leave History & Attendance Report Enhancement	Live
Release 4.4	CSS	Banan	—	—	• Gift Disclosure Enhancement • Payslip Design Enhancement - MOCASmart • Hajj Leave Enhancement • Personalized Eid Al Adha Greeting Link • Survey Push Notification	Live
Release 4.3	CSS	Banan	—	—	• Vendor Catalog & Tiers Enhancement • Reject Requests (Petty Cash, Reimbursement, Credit Card) • Employee Address Update • Enhancing the Submission for Compassionate Leave • Survey Push Notification	Live

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Release 4.2	CSS	Banan	—	—	- News & Announcements - Absence Statistics (Check-In & Check-Out Time) - WFH Check-In / Check-Out	Live
Release 4.1	CSS	Ghaya	—	—	- Duaa Popup Feature - TMS Guide on MOCASmart - Gift Disclosure Integration with Oracle	Live
Release 4	CSS	Ghaya	—	—	- Pop-up for Pending Justification - Change Password Feature - Policies Section - Duaa Icon & Push Notification - Relative Declaration Card	Live
Release 3	CSS	Banan	—	—	Released and in production	Live

Section 03

Demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Decrees (HR Services)	CSS	Banan	- With Business - New demo conducted for template feature on GovSign - HR liked this feature and would like to proceed	Await chief approval	With Business
HR Requests (Job Description Icon & Oracle Integration, Employee Benefits, Contracts and Acknowledgment page)	CSS	Banan	- Under Scope Analysis - HR confirmation is required to finalize the SOW	- Obtain the vendor's cost and time estimate - Obtain cost approval to proceed	Under Scope Analysis
MBRGEA Agentic AI	PMO	Banan	- Under Scope Analysis - The final SOW has been shared with the business and Kalvad team to schedule a meeting and align on next steps.	Get proposal from Kalvad team	Under Scope Analysis
SKGEP Enhancement	PMO	Banan	- Under Scope Analysis - Received feedback from Kalvad: rebuild the web rather than perform the enhancement because the site uses old technology. - Asked the vendor to submit their proposal.	Receive a proposal and proceed accordingly	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Talent Management System/ Development	CSS	Banan	- Under Scope Analysis - Waiting for TenTwenty to share the document so we can finalize the scope.	Share the final SOW that matches the final design	Under Scope Analysis
Application Development for Government Relations & Protocol Department	CSS	Noura	- Under Scope Analysis - We have shared the proposal and proposals comparison with business team	Waiting for business direction	Under Scope Analysis
Assets requests	CSS	Noura	- Under Scope Analysis - We had a meeting with Motion Pexels and the business team to review the solution and gather their feedback.	- Motion Pexels team will share the technical proposal, initial plan and cost that includes AI recommendations. - Saif and Shaikha will provide details of existing systems and API access information for Span, and other data sources to enable integrations. - Saif & Shaikha will send a sample of the client's data.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Automating the department achievements report - Injaz-Enhancement	CSS	Noura	- Proposal Review - We received the proposal from kalvad team.	- We have shared the proposal with business - Multiple meetings were held with the business team and design team to discuss the Scope of Work. Additional changes have been requested, and once the...	Proposal Review
Avatar Ai Phase 2	PMO	Noura	- Under Scope Analysis - Explored the possibility of replicating the current avatar (same look and feel) to enable simultaneous deployment across multiple government... - The objective is to evolve the avatar from a single “minister” persona into an advisor supporting multiple ministers or government leadership teams. - Replicating the solution as a UAE national persona by adapting the avatar’s appearance and accent, while maintaining the same advisory function and...	Business team is awaiting vendor feedback on the previously shared questions regarding the proposed change of persona from "Minister" to "Advisor",...	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Breathable Infrastructure Competition Website	PMO	Noura	- In Progress - Reviewed the proposed website and confirmed it will be a single-page public website with competition details, key dates, prize information, and... - The website will be developed and hosted within the existing environment. - Cybersecurity requested an architecture diagram covering the hosting setup, DNS/URLs, CMS, and external platform redirection.	- Santhosh to prepare and share the architecture diagram, including the external URL redirection and DNS details. - Madhu to review the architecture and share a focused set of security questions/requirements. - Once the staging environment is ready, Cybersecurity will proceed with the VA/PT assessment.	In Progress
Demand & Digital Transformation Services in MOCA App	CSS	Noura	- Under Scope Analysis - We had a meeting with Kalvad team to go through the design and SOW.	- We need to check with business if we will use Ivanti or Jira - Check if we will use the AI chatbot for the project requests	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Ems Phase 2	CSS	Noura	- Under Scope Analysis - We had meeting with Evento team to discuss the redesign scope for the untested features that will be implemented. - The Agentic AI SOW was shared with the Evento team to review its feasibility. The team will check and confirm if it is doable.	- It was agreed that the work will be divided into three separate scopes: # System Redesign & Admin Page – No Additional Cost # Redesign of the existing system.	Under Scope Analysis
GA Agentic AI Coach	PMO	Noura	- Under Scope Analysis - We had two separate meeting with IT and cybersecurity team to kickoff the project.	- Capgemini team has shared the architecture design, list of questions, and details of the LLMs to be reviewed by shamma. - The project team will share the security questionnaire and data classification documents.	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Photographer and Videographer Requests (EMS and MOCA App)	CSS	Noura	- Under Scope Analysis - MOCA Smart will be used by employees to submit requests for photographers and videographers. - Admin users in EMS will be able to add/edit photographer and videographer schedules and show their leaves from Oracle. - In EMS, photographers will have the option to click “Start Job” when they begin and “End Job” upon completion.	- The business team has decided to include Agentic AI in the project scope. We are currently updating the Scope of Work (SOW) and will share the... - Kalvad has shared the estimate, and we will have meeting tomorrow to discuss the AI part.	Under Scope Analysis
Store Management System	CSS	Noura	- RFI - Proposals comparison are submitted to business	We are waiting for business directions.	RFI
Adaa Agentic AI Use Cases	PMO	Zeyad	In Progress	Confirm next step with the demand owner	In Progress
Automating the Cabinet Health-Check Process	GSOC	Zeyad	- Under Scope Analysis - Scope and design has been highlighted to the vendor, and we expect the first release to be on July-2026	Having live demo with business once the release to deployed	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Data Management Agentic AI Use Cases	PMO	Zeyad	In Progress	Confirm next step with the demand owner	In Progress
Agentic AI - Finance MVP -PWC	CSS	Manju	- Under Scope Analysis - PWC briefed on the MVP requirements for finance - PWC requested for Budget control and I2P demo call on Thursday 10th Sep	- Finance to confirm which process from budgeting they will be using for MVP - Schedule the demo meeting upon confirmation	Under Scope Analysis
Agentic AI - P2P MVP -1001	CSS	Manju	- Under Scope Analysis - Shared the relevant Oracle API access and LLM, embedding model details. - Aligned with IT and Security - Oracle application access issue is being addressed with networks team	- Completed APIs are being progressively handed over to the vendor (1001) for further development. - Resolve the Oracle application access issue and other impediments arising during development	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Agentic AI - P2P MVP -Cohere	CSS	Manju	- Under Scope Analysis - Account creation completed; VPN and other relevant access permissions granted - Alignment meetings completed with the IT, Security, Oracle, and Business teams. - Shared the relevant Oracle API access and LLM details.	- Initiate MVP development planning. - Resolve the Oracle application access issue and other impediments arising during development	Under Scope Analysis
Agentic AI - P2P MVP -Inception	CSS	Manju	- Under Scope Analysis - Alignment meeting held with IT, Security and Oracle team - Account creation in progress	- Inception to come back with architecture and infrastructure plan for on-prem hosting - Inception to share security questionnaire for assessment	Under Scope Analysis
Agentic AI - Payroll MVP -Aleria	CSS	Manju	- Under Scope Analysis - To schedule a meeting with Aleria and we are waiting for their confirmation	Based on meeting outcome we will proceed	Under Scope Analysis

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
WGS DR 2026	WGS	Manju	- Under Scope Analysis - Initial alignment with IT, Security, TenTwenty and Evento team held. - Security Requirement Document Shared with WGS - IT team has requested meeting with Vendor IT	- Essa to confirm on the meeting schedule - WGS to share the open IT/Security questionnaire with Innova.	Under Scope Analysis

Section 04

Live projects

Project Name	Entity / Sector	PM	Go-Live
APEX- Off-Boarding	CSS	Banan	8 May 2026
APEX- Probation Extention	CSS	Banan	20 Mar 2026
APEX- Relative Declaration	CSS	Banan	9 Mar 2026
API Migration to OIC (FORAS)	CSS	Banan	4 Dec 2025
API Migration to OIC (MocaVerse)	CSS	Banan	31 Dec 2025
DOR	CSS	Banan	18 Mar 2026
Enhancing MOCA Letters	CSS	Banan	1 Apr 2026
Events Calendar (MOCAverse)	CSS	Banan	28 Apr 2026
Executive Dashboard Release 2-Enhancment	CSS	Banan	13 May 2026
Government Accelerator Website	PMO	Banan	30 Apr 2026
Interactive Dashboard/Event website	GSOC	Banan	31 Aug 2026
MOCA SSA	CSS	Banan	11 May 2026
MOHAP Sick Leave Integration	CSS	Banan	24 Jul 2026
NER	CSS	Banan	Live
Organization Structure (HR Services)	CSS	Banan	3 Aug 2026
Talent Hub MBRCGI	Strategy & Innovation	Banan	Live
Vendor Dashboard	CSS	Banan	15 May 2026
Vendor Management - NER Enhancement	CSS	Banan	29 Jul 2026
WGS-Website	WGS	Banan	19 Jan 2026

Project Name	Entity / Sector	PM	Go-Live
Gift Disclosure Enhancment	CSS	Ghaya	12 May 2026
Avatar AI	PMO	Noura	31 Mar 2026
Event Management System	CSS	Noura	9 Apr 2025
Customer Pulse	Performance & Govt Excellence	Shamma	31 Dec 2025
AGEA System	Performance & Govt Excellence	Zeyad	12 Dec 2025
Candidate Recruitment Committee Website	GSOC	Zeyad	30 Sep 2026
GEEP	GEEO	Zeyad	15 May 2026
GSOC emp worksheet	GSOC	Zeyad	15 May 2026
Innovation Ecosystem	Strategy & Innovation	Zeyad	24 Nov 2025
SecureAware Platform	CSS	Zeyad	31 Aug 2026

Section 05

On hold / not active

Project Name	Entity / Sector	PM	Current Status	Next Steps	Project Outcome	Go Live
Digital Library	CSS	Noura	- On Hold - We had a meeting with the AI Office and the vendor to review the proposed solution. - During the discussion, Saqr suggested adding an MCP layer on top of the solution. This would simplify future integrations and enhance the scalability... - As an example, if Fouzia asks:	- The Media Info team will confirm if adding the MCP layer is feasible - Khawla will start filter the content - Kickoff meeting	—	TBD — not yet baselined
FAHR sick leave Integration	CSS	Banan	- On Hold - On Hold due to Agentic AI P2P project	Resume development	To have integration real time with sick leave with committee approvals	23 Nov 2026
Media Monitoring & Public Feedback Intelligence Platform	PMO	Zeyad	- On Hold - Vendor evaluation in under process by business users and procurement. reminder sent to business. there is some issue in the budgeting.	- Finalize the vendor evaluation process with business users. - If there is no update from budgeting will move this project to on-hold until budget allocated.	Enhance the quality, responsiveness, and customer-centricity of government services across the UAE by observing and...	TBD — under technical evaluation; plan not provided
Project Dashboard in Executive Dashboard	CSS	Shamma	- On Hold - Waiting for the developer budget to be approved to onboard the developer	Once budget approved onboarding the developer to kick off the project	—	TBD — not yet baselined

Section 06

Not active / closed demands

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Executive Dashboard Sprint 3	CSS	Banan	- Not active - Fouzia approved to do development once new developer onboarded	Once developer joined a plan will created for development	Not active as we are waiting if we will hire developer or with AI
Onboarding (HR Services)	CSS	Banan	- Not active - Met with Ali to discuss next steps - We will await confirmation on whether this service will fall within the scope of the Agentic AI project.	- Once a direction is provided, we will determine how to proceed accordingly. - Not active	Not active waiting for business direction
Payroll Bot Implementation	CSS	Banan	- Not active - On hold	To select vendor	Not active moving to new platform
Peer Assignment System	CSS	Banan	- Not active - Awaiting internal confirmation	Not Active	Not active as we are waiting for HR confirmation
Promotion Project	CSS	Banan	- Not active - Created draft SOW and shared with Business for approval - Requested additional information needed to finalize the SOW	Finalize SOW and start the development	Not active — automate the employee promotion/increment process by enhancing the existing Oracle Apex...
Remote Work Balance for GMO	GMO	Banan	- Not active - GMO study completed; shared with Ali	Await direction	Not Active as we are waiting for HR direction

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Security Form (Data Classification)	CSS	Banan	- Not active - Received the initial design from the UX team - Send the presentation to Moza to schedule a meeting with Fouzia.	- Present to Fouzia the initial design. - Project team will draft the initial SOW after Fouzia's approval on the design. - The implementation of the form will be based on the old criteria until the new policy is approved	Not Active as we are waiting for direction
So Lite	PMO	Banan	- Not active - The technical team confirmed a resource is available for use and received from the business team; no support is required at this stage.	Confirm next step with the demand owner	Not active — lite version from observatory system
Working Remotely Enhancement	CSS	Banan	Not active	Confirm next step with the demand owner	Not active — project Team need to reactive this request with HR
X Employee Project	CSS	Banan	- Not active - The project on hold due to Agentic AI P2P	Confirm next step with the demand owner	Not active — pull employee data from Oracle using predefined questions and answers, analyze it to generate...
Audio Translator in Teams	CSS	Noura	- Not active - The proposals were received and shared with the business for feedback	Confirm next step with the demand owner	Not active as per business direction

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Synthetic Memories UAE	PMO	Noura	- Not active - The vendor is still finalizing the proposal	We are waiting for an update from the business	Not active as per business direction
Tech Trial AWS	PMO	Noura	- Not active - The project is currently with IBM and in the design presentation phase for leadership - We recommended the business to go through the proposal with the IT and cybersecurity teams before presenting	Arrange two separate meetings with the IT and Cybersecurity teams to review the requirements	Not active as per business direction
Customer Pulse Integration with Jira	CSS	Shamma	Not active	Confirm next step with the demand owner	Not active moving to new platform
Acting project	CSS	Manju	- Not active - The project has been postponed at the Business's request	- Once the project is active - get the SOW approval from Business - Commence the development	Not active — to handle acting positions and decisions

Demand / Request	Entity / Sector	PM	Current Status	Next Steps	Status
Digital Transformation Project Portfolio for chief	CSS	Manju	- Not active - We have now the link via claude we are exploring how we can host on our environment - Meeting with IT & security to discuss requirements - Security and Application team have a few open queries that needs to be addressed by Hana	Finalize the project requirement and prepare the SOW document	Not active — to have a dashboard for the chief where she can see 3 reports weekly: WGS Report CSS projects...
Job description Agent	CSS	Manju	- Not active - Evaluating the scope and gathering project requirements from the Business. - Oracle team validating the requirements and confirming the feasibility.	Finalize the development approach and SOW, and initiate development.	Not active — to create Job description for all the employees
WGS Evento/Registration	WGS	Manju	- Not active - Initial meeting with WGSxEvento held and MOM shared	Finalize the SOW, project plan and start the development	Not active — simplify and enhance the WGS registration process
